

HART

HONOLULU AUTHORITY for RAPID TRANSPORTATION

Construction and Traffic Update September 24th, 2015

H O N O L U L U R A I L T R A N S I T P R O J E C T

WWW.HONOLULUTRANSIT.ORG

HART

HONOLULU AUTHORITY for RAPID TRANSPORTATION

Project Map

20 Miles – 21 Stations



Rail Operations Center Design-Build



Physical Construction Completion	80%
Contract Billed to Date	79%
Contract Billing Planned Per Schedule	85%

** ROC construction currently tracking to the planned Substantial Completion date.*

** Contractors Billings may lag behind physical work completed due to milestone based payment contract.*

Operations Services Building (OSB)



H O N O L U L U R A I L T R A N S I T P R O J E C T

www.HONOLULUTRANSIT.ORG

HART
HONOLULU AUTHORITY FOR RAPID TRANSPORTATION

Maintenance of Way (MOW) Building



H O N O L U L U R A I L T R A N S I T P R O J E C T

www.HONOLULUTRANSIT.ORG

HART

HONOLULU AUTHORITY FOR RAPID TRANSPORTATION

Wheel Truing Building (WTB)




H O N O L U L U R A I L T R A N S I T P R O J E C T


www.HONOLULUTRANSIT.ORG

HART
HONOLULU AUTHORITY for RAPID TRANSPORTATION

Train Wash Facility (TWF)

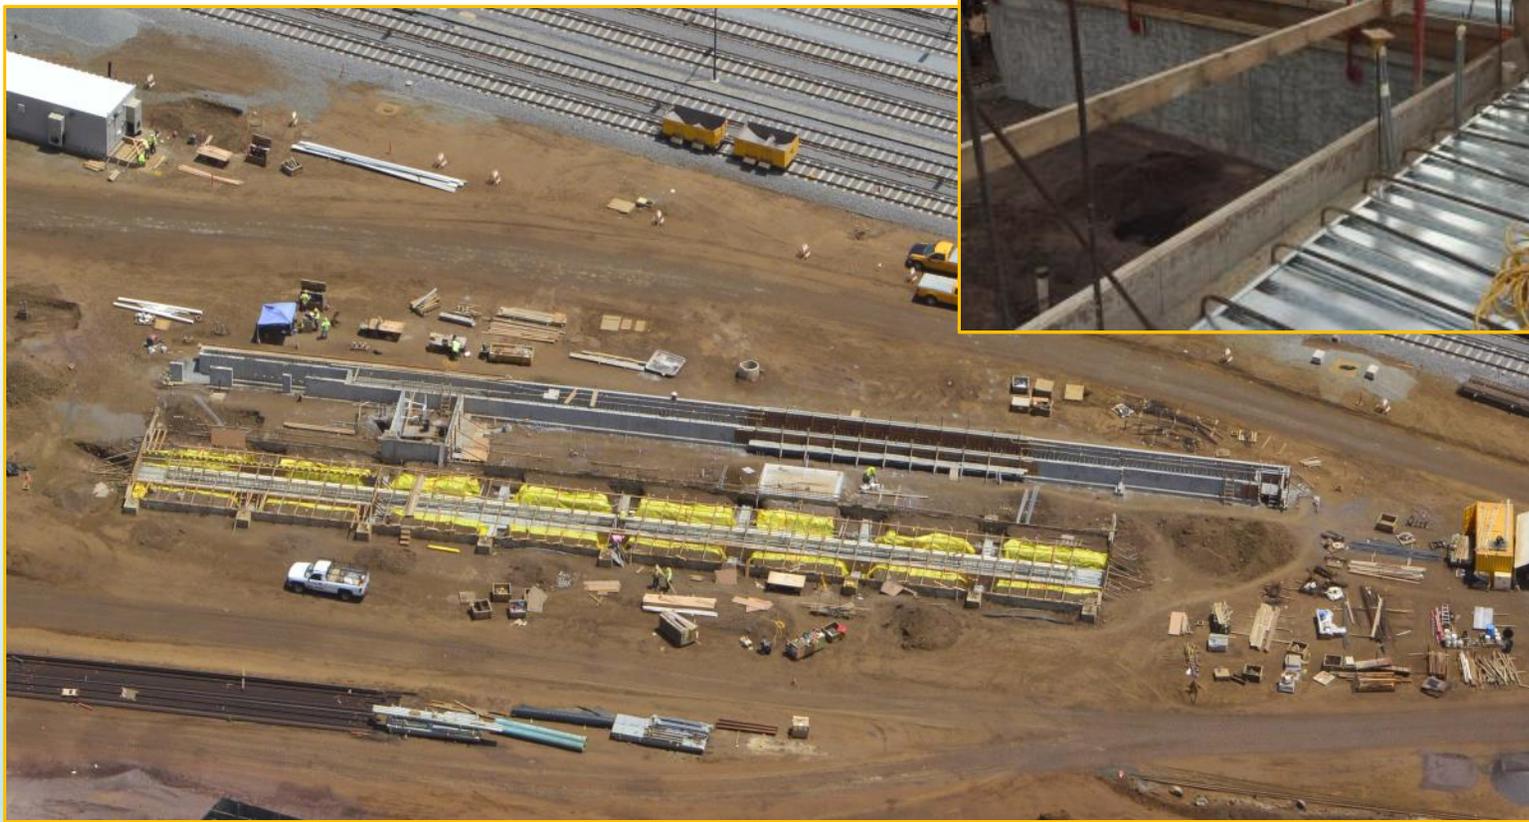

Rail Operations Center Trackwork

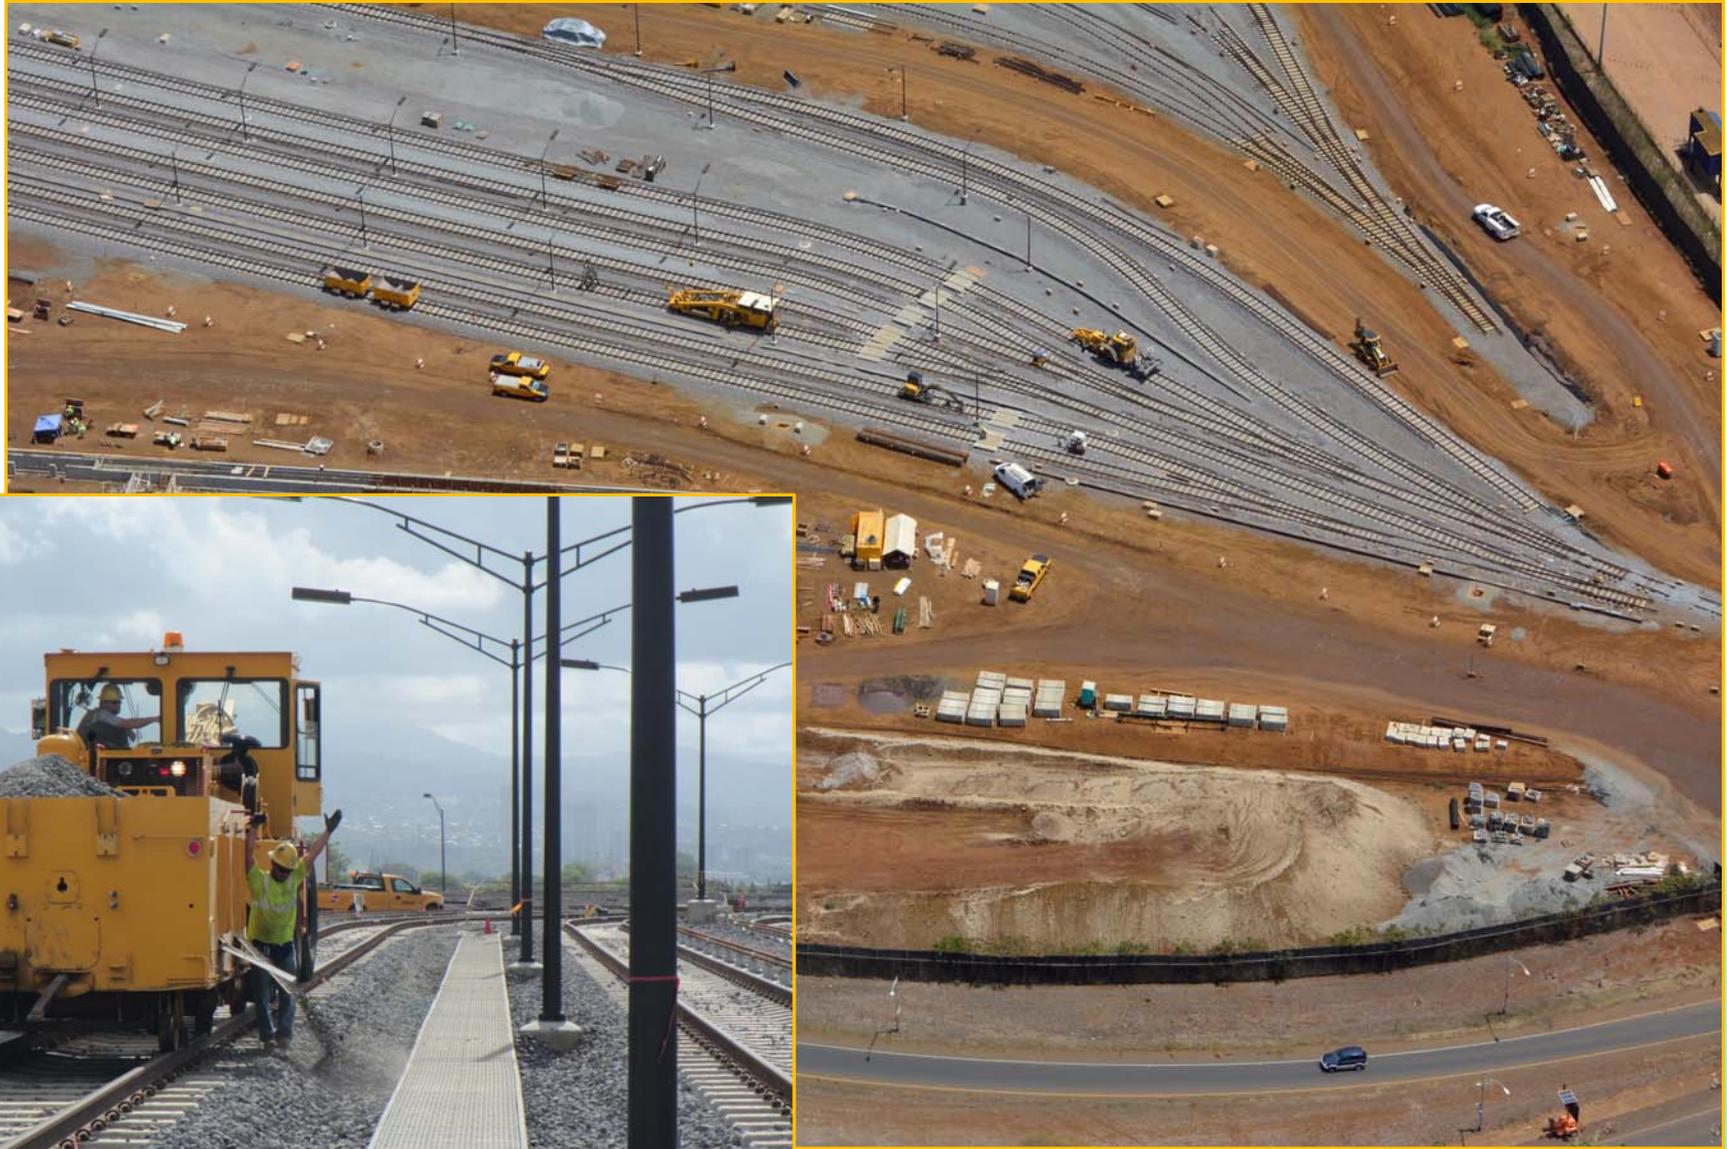

H O N O L U L U R A I L T R A N S I T P R O J E C T

www.HONOLULUTRANSIT.ORG

HART

HONOLULU AUTHORITY for RAPID TRANSPORTATION

West Oahu Farrington HWY Guideway

Construction Completion 71.7%

Contract Billed to Date 69.9%

Contract Billing Planned Per Schedule 81.33

- *WOFH construction currently tracking 4 - 6 months behind the planned Substantial Completion date.*

** Contractors Billings lag behind physical work completed due to milestone based payment contract.*



H O N O L U L U R A I L T R A N S I T P R O J E C T

www.HONOLULUTRANSIT.ORG

HART

HONOLULU AUTHORITY for RAPID TRANSPORTATION

Balanced Cantilever Work



H O N O L U L U R A I L T R A N S I T P R O J E C T

www.HONOLULUTRANSIT.ORG

HART

HONOLULU AUTHORITY for RAPID TRANSPORTATION

KHG Design-Build



Physical Construction Completion	39.6%
Contract Billed to Date	35.9%
Contract Billing Planned Per Schedule	84%

- *KHG construction currently tracking 6-7 months behind the planned Substantial Completion date.*



Farrington HWY Stations

Construction Completion **0%**
Contract Billed to Date **0%**
Contract Billing Planned Per Schedule **0%**

- *Notice to Proceed (NTP) Issued*
- *Ground Breakings being scheduled*



H2R2 Ramp

Construction Completion 0%
Contract Billed to Date 0%
Contract Billing Planned Per Schedule 0%

- *Contract awarded to Royal Contracting*
- *Notice to Proceed (NTP) Issued*
- *Preconstruction Submittals and Permitting*



West Oahu Stations

Construction Completion **0%**
Contract Billed to Date **0%**
Contract Billing Planned Per Schedule **0%**

- *Notice to Proceed (NTP) Issued*
- *Ground Breakings being scheduled*



Moving Forward: The Next 10 Miles



Airport Advanced Utilities

Physical Construction Completion 16.8%

Contract Billed to Date 15.7%

- *Airport Section Utility Construction currently is tracking 7 months behind the planned Substantial Completion date.*



Airport 7 Piers

Physical Construction Completion 100%

Contract Billed to Date 84.0%

- *Airport 7-Piers Contract is currently being closed out.*

Traffic Update



H O N O L U L U R A I L T R A N S I T P R O J E C T

www.HONOLULUTRANSIT.ORG

HART
HONOLULU AUTHORITY FOR RAPID TRANSPORTATION

Farrington Highway in Waipahu




H O N O L U L U R A I L T R A N S I T P R O J E C T

www.HONOLULUTRANSIT.ORG

HART

HONOLULU AUTHORITY FOR RAPID TRANSPORTATION

Farrington Highway in Waipahu

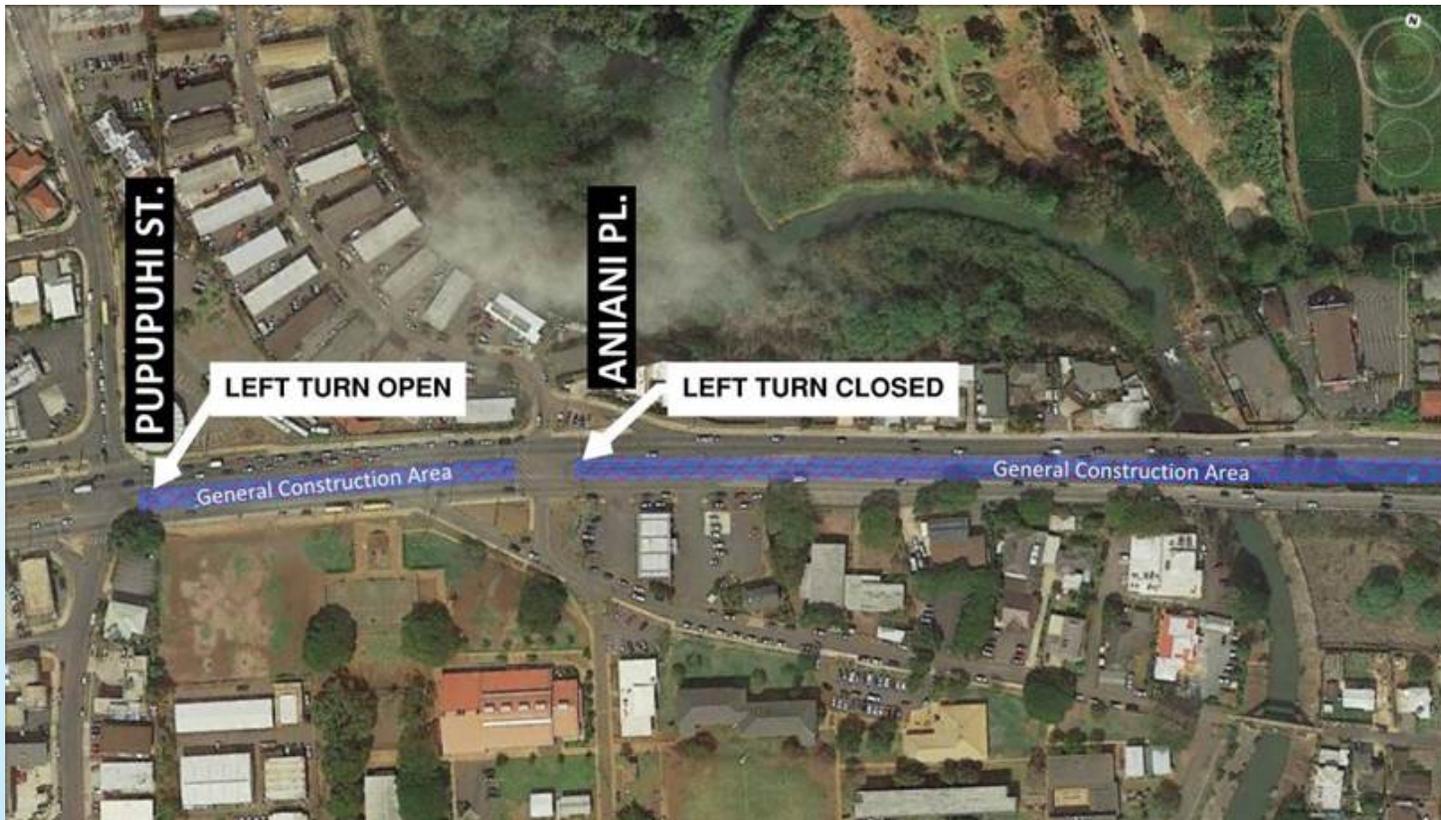


Farrington Highway in Waipahu




Farrington Highway in Waipahu




Balanced Cantilever Work

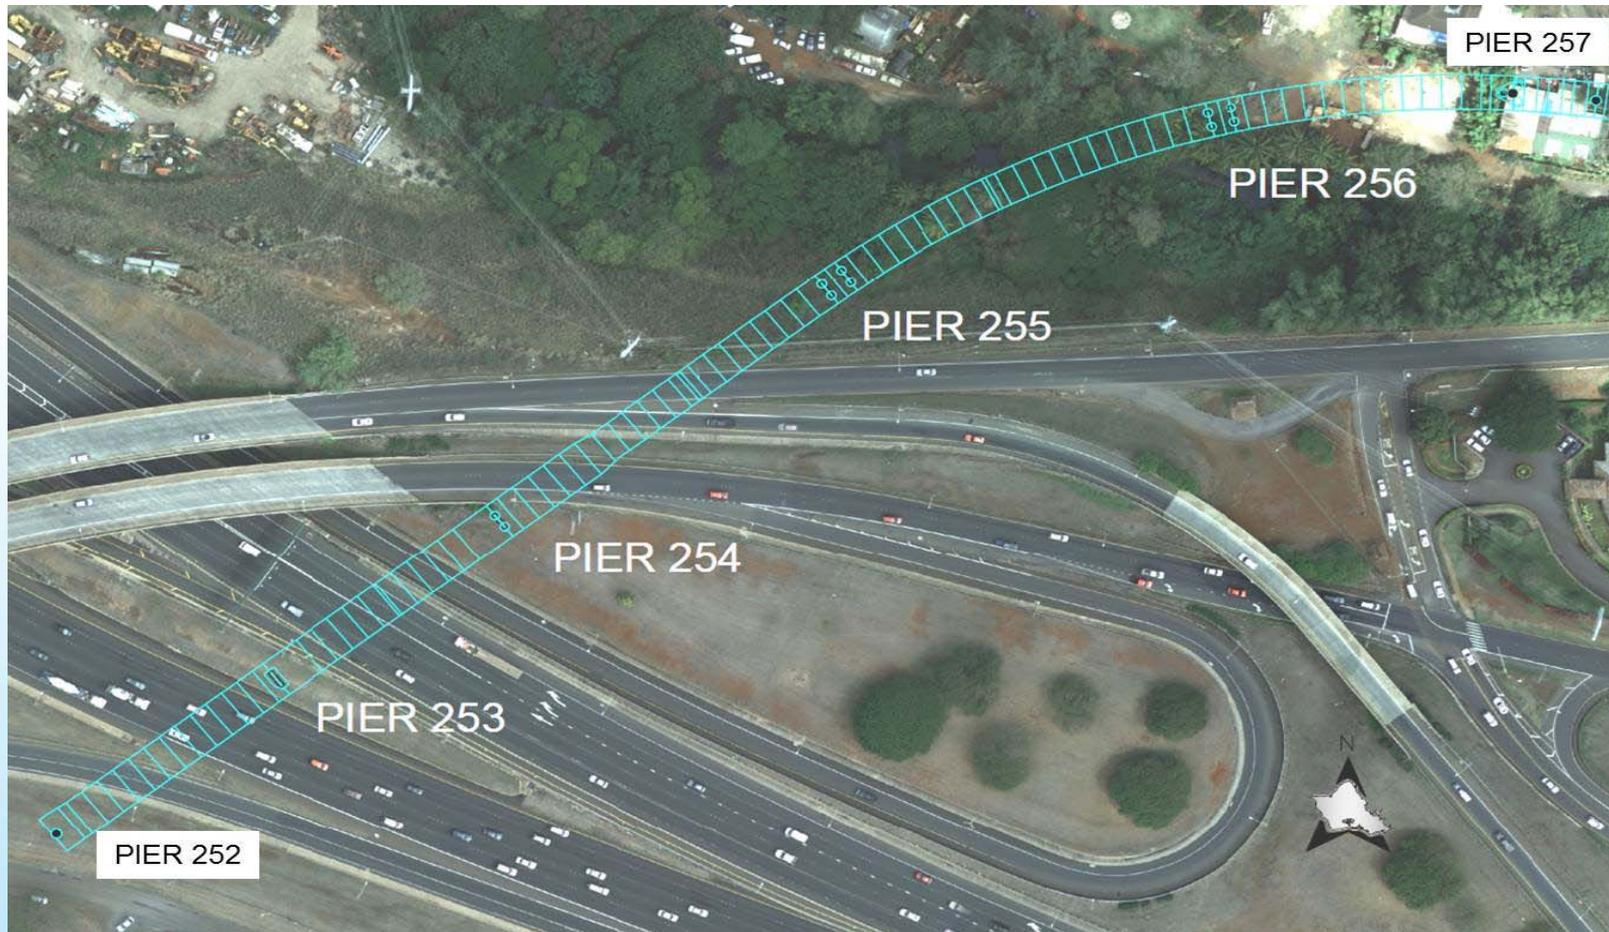


Kamehameha Highway in Pearl City

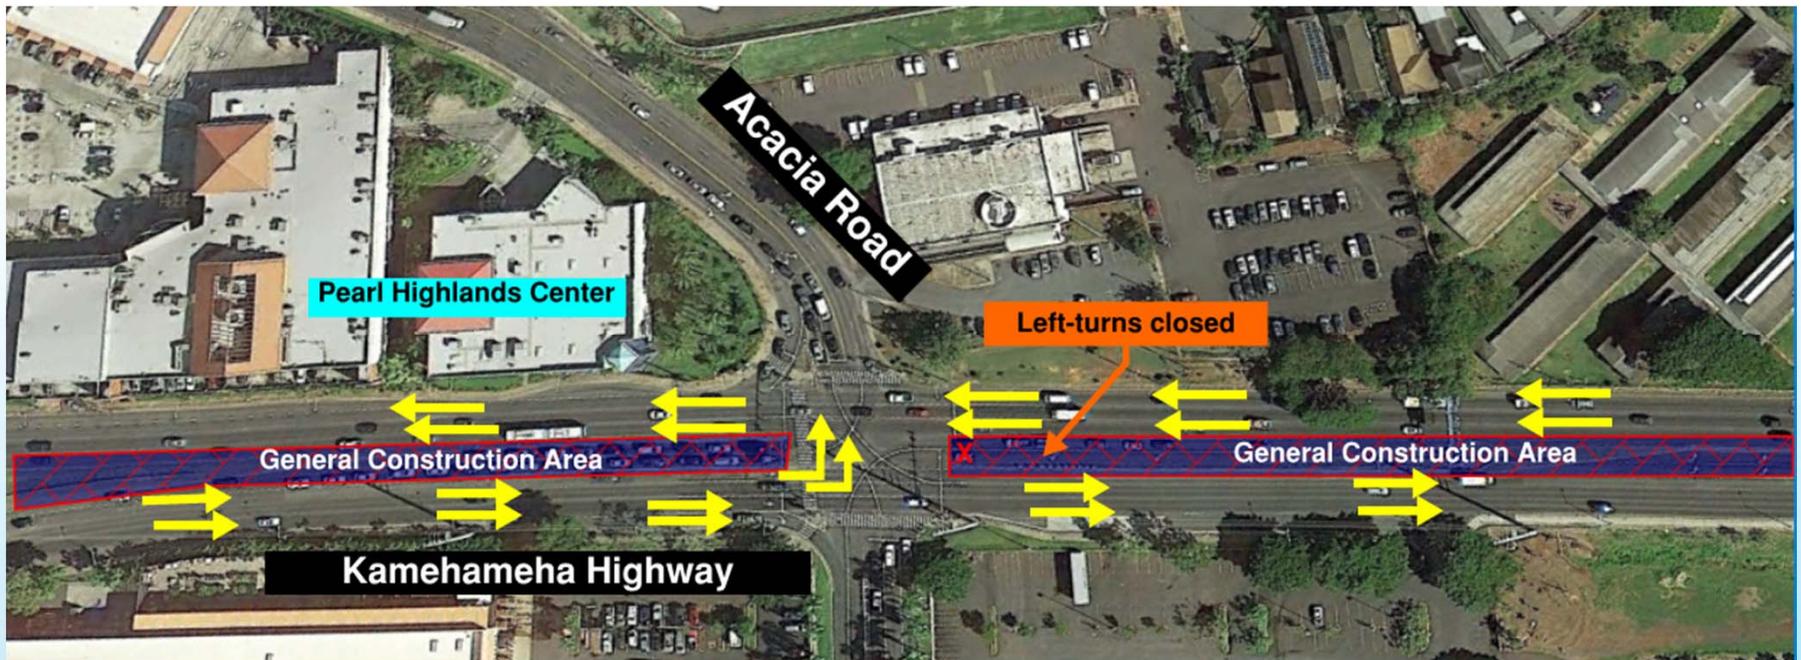

Kamehameha Highway in Pearl City

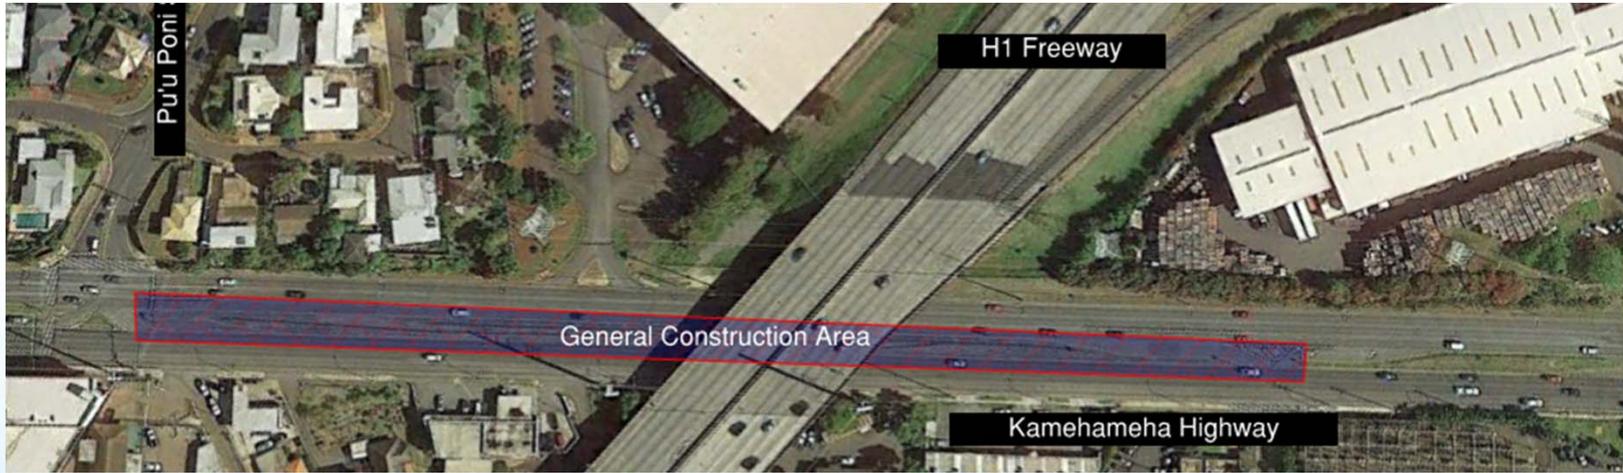

Kamehameha Highway near Pearl Harbor

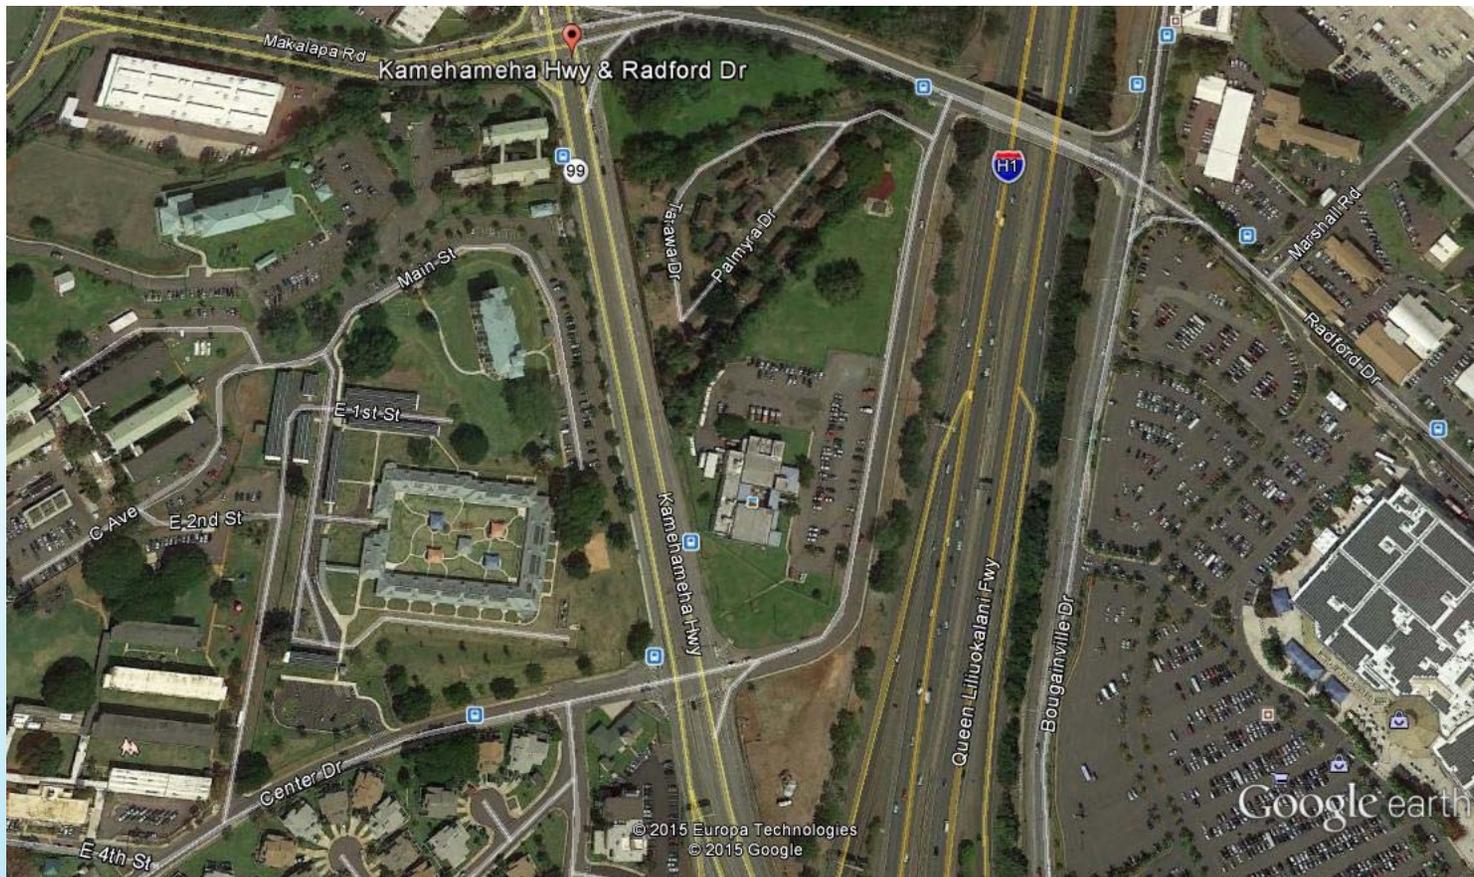

Mahalo!



HONOLULU RAIL TRANSIT

H O N O L U L U R A I L T R A N S I T P R O J E C T

www.HONOLULUTRANSIT.ORG

HART

HONOLULU AUTHORITY for RAPID TRANSPORTATION
