

HART

HONOLULU AUTHORITY for RAPID TRANSPORTATION

Construction and Traffic Update June 25th, 2015

H O N O L U L U R A I L T R A N S I T P R O J E C T

WWW.HONOLULUTRANSIT.ORG

HART

HONOLULU AUTHORITY for RAPID TRANSPORTATION

Project Map

20 Miles – 21 Stations



Rail Operations Center Design-Build



Physical Construction Completion	72%
Contract Billed to Date	75%
Contract Billing Planned Per Schedule	80%

** ROC construction currently tracking to the planned Substantial Completion date.*

** Contractors Billings may lag behind physical work completed due to milestone based payment contract.*

Operations Services Building (OSB)



H O N O L U L U R A I L T R A N S I T P R O J E C T

www.HONOLULUTRANSIT.ORG

HART
HONOLULU AUTHORITY FOR RAPID TRANSPORTATION

Maintenance of Way (MOW) Building



Train Wash Facility (TWF)



Rail Operations Center Trackwork



H O N O L U L U R A I L T R A N S I T P R O J E C T

www.HONOLULUTRANSIT.ORG

HART

HONOLULU AUTHORITY FOR RAPID TRANSPORTATION

West Oahu Farrington HWY Guideway

Construction Completion 64%

Contract Billed to Date 64%

Contract Billing Planned Per Schedule 75.7%

- *WOFH construction currently tracking 4 - 6 months behind the planned Substantial Completion date.*
- *Contractors RFC for Time Extension recently submitted and is currently under review.*



H O N O L U L U R A I L T R A N S I T P R O J E C T

www.HONOLULUTRANSIT.ORG

HART

HONOLULU AUTHORITY FOR RAPID TRANSPORTATION

Balanced Cantilever Work



KHG Design-Build



Physical Construction Completion	38%
Contract Billed to Date	37%
Contract Billing Planned Per Schedule	76%

- *KHG construction currently tracking 6-7 months behind the planned Substantial Completion date.*
- *Lack of HECO Productivity Creating the potential additional schedule impacts.*
- *Contractors RFC for Time Extension schedule for submittal in July.*



Farrington HWY Stations

Construction Completion 0%

Contract Billed to Date 0%

Contract Billing Planned Per Schedule 0%

- *Contract awarded to Hawaiian Dredging*
- *Kickoff and Preconstruction Meeting being scheduled*
- *Notice to Proceed (NTP) forthcoming*



H2R2 Ramp

Construction Completion 0%
Contract Billed to Date 0%
Contract Billing Planned Per Schedule 0%

- *Contract awarded to Royal Contracting*
- *Kickoff and Preconstruction Meeting*
- *Notice to Proceed (NTP) Issued*



Pearl Highlands Station

Moving Forward: The Next 10 Miles



Airport Advanced Utilities

Physical Construction Completion 16.78%

Contract Billed to Date 8.82%

- *Airport Section Utility Construction currently is tracking 5 months behind the planned Substantial Completion date due to Navy right-of-entry issues.*
- *The Navy has recently released right-of-entry for construction activities to commence.*
- *HART Noise variance has been submitted to DOH for approval.*

Airport 7 Piers

Physical Construction Completion 100%

Contract Billed to Date 84.0%

- *Airport 7-Piers Contract is currently being closed out.*
- *Site has been turned over to HDOT Airport.*



Traffic Update



H O N O L U L U R A I L T R A N S I T P R O J E C T

www.HONOLULUTRANSIT.ORG

HART
HONOLULU AUTHORITY FOR RAPID TRANSPORTATION

Farrington Highway Detour




Farrington Highway in Waipahu




Farrington Highway in Waipahu



Balanced Cantilever Work

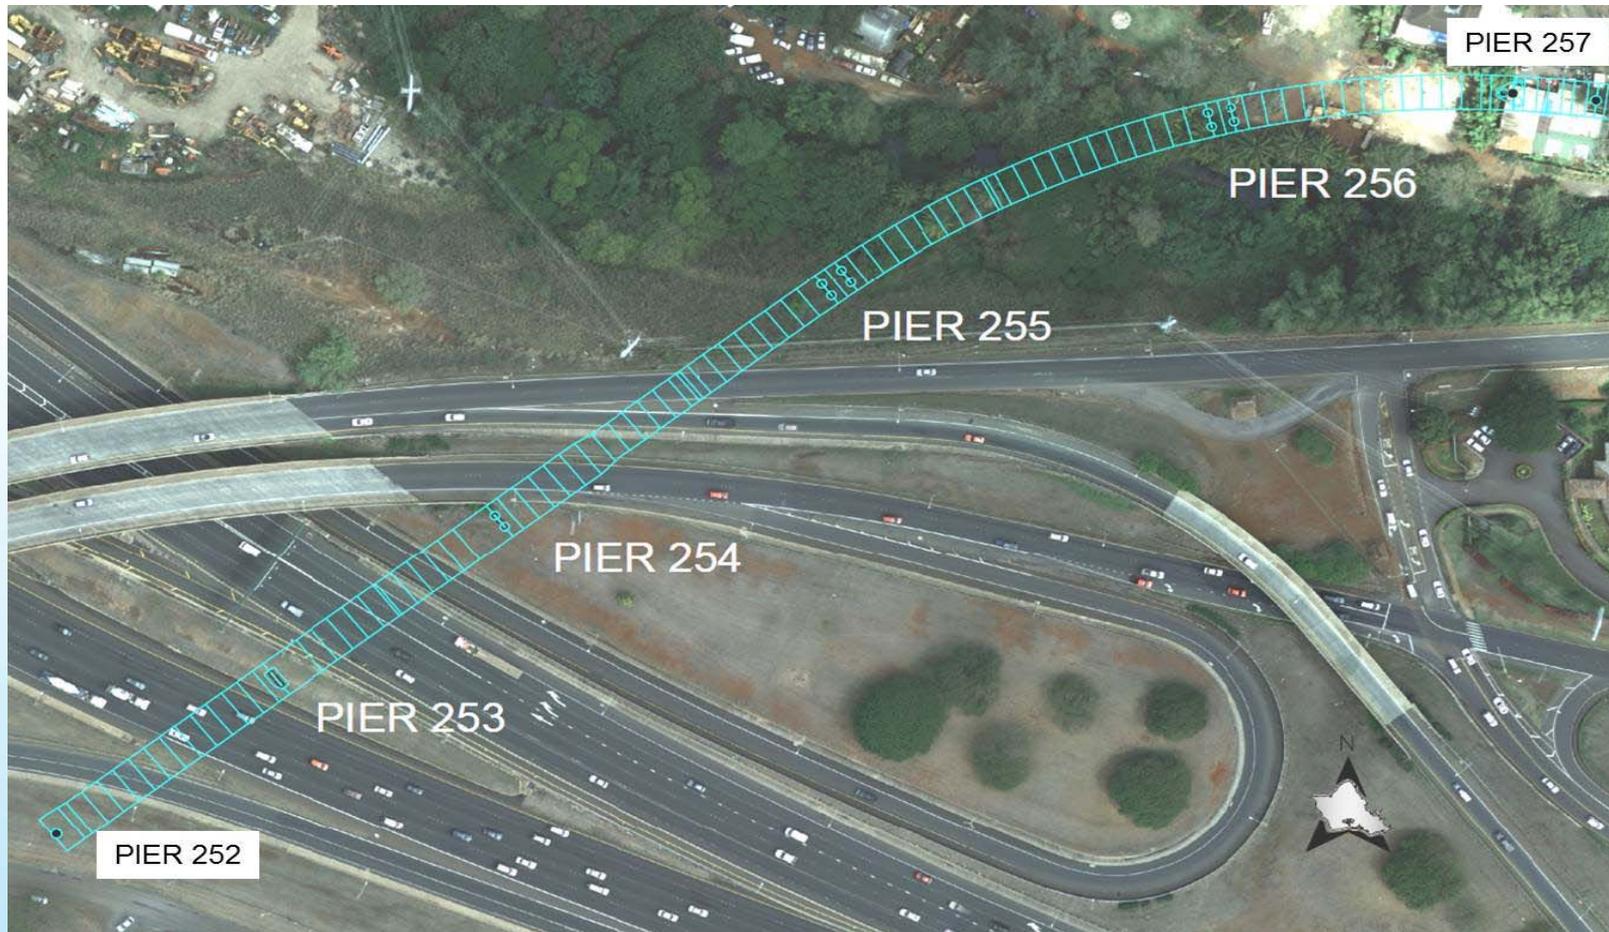

Balanced Cantilever Work

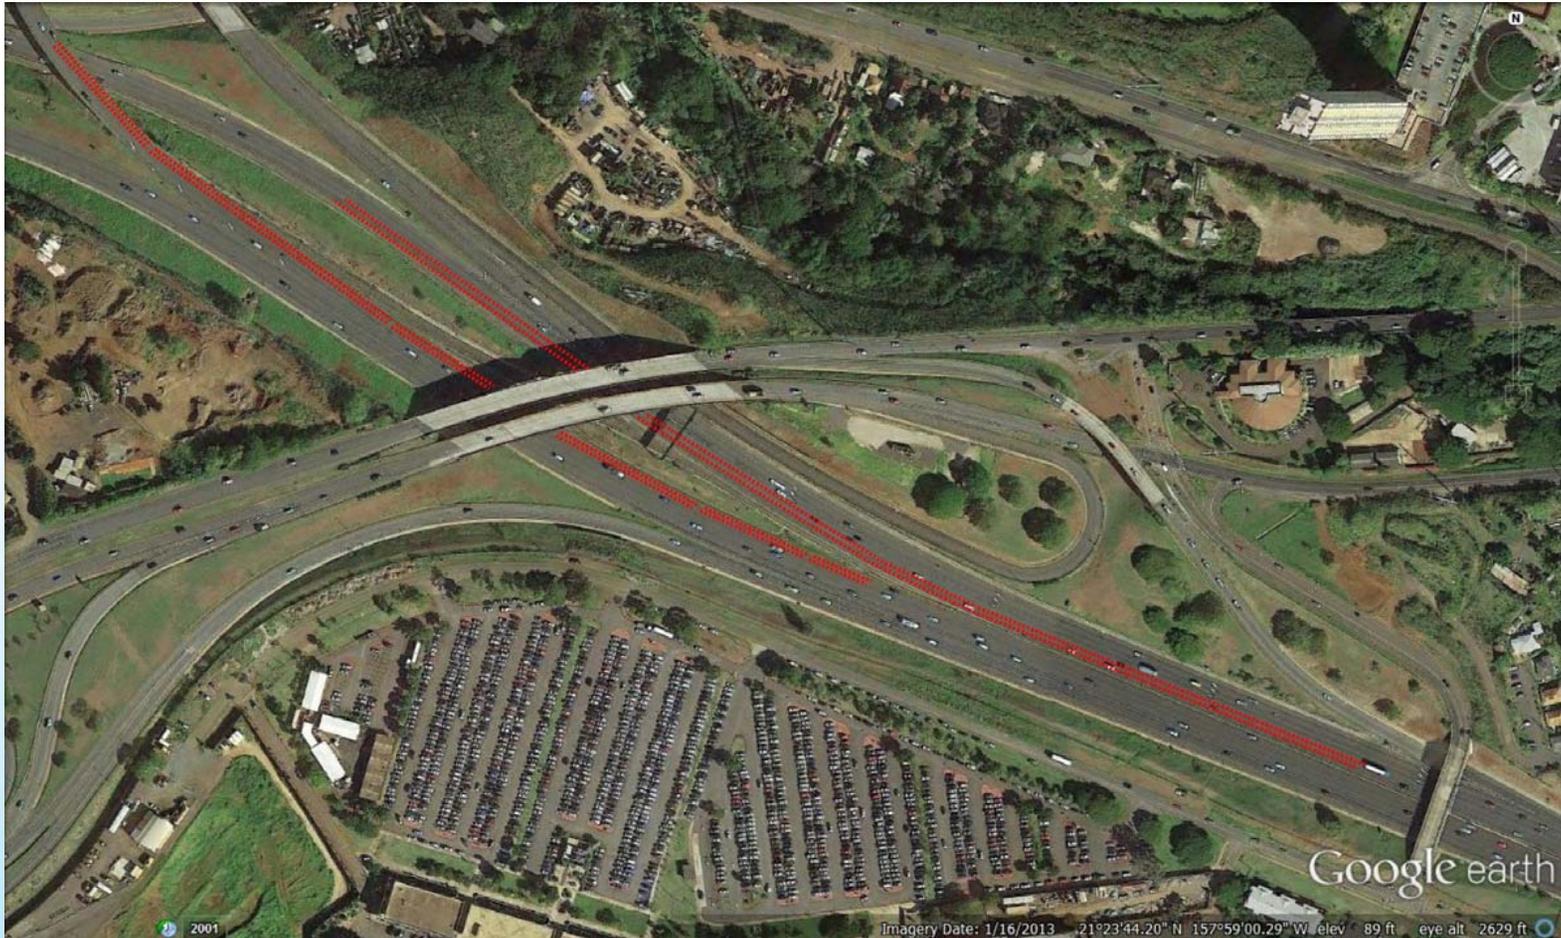


H O N O L U L U R A I L T R A N S I T P R O J E C T

www.HONOLULUTRANSIT.ORG


HART

HONOLULU AUTHORITY FOR RAPID TRANSPORTATION


Kamehameha Highway in Pearl City

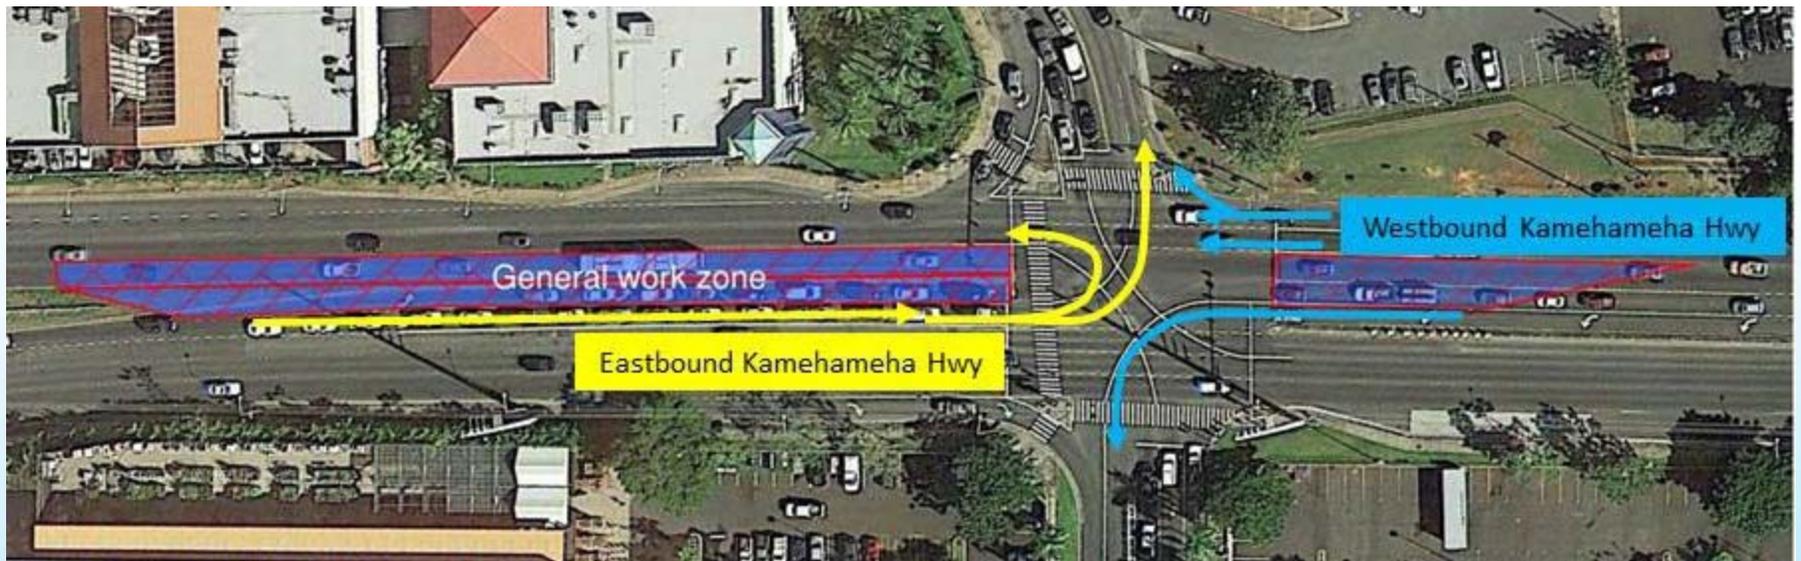


Kamehameha Highway in Pearl City

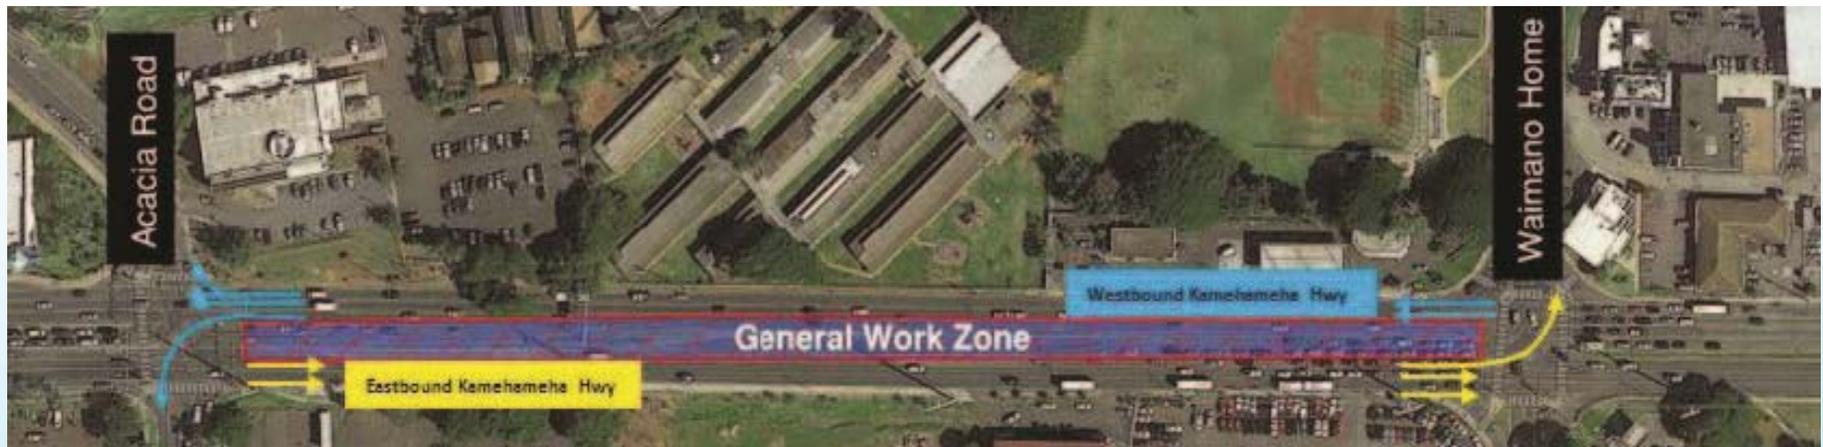


Kamehameha Highway in Pearl City

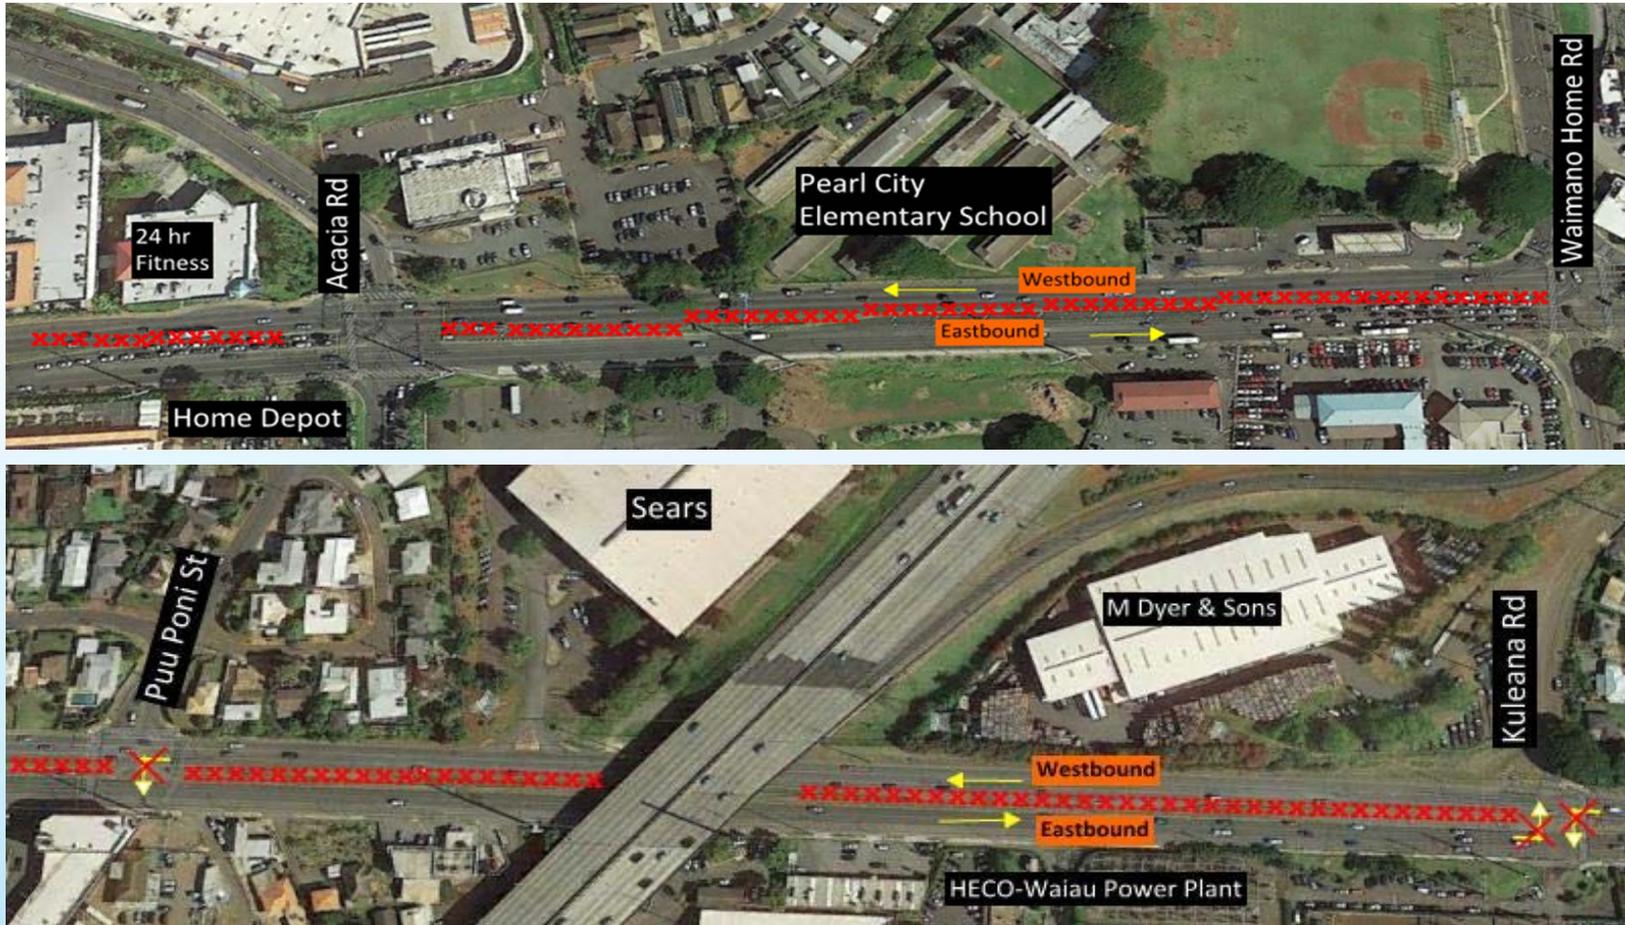


Kamehameha Highway in Aiea

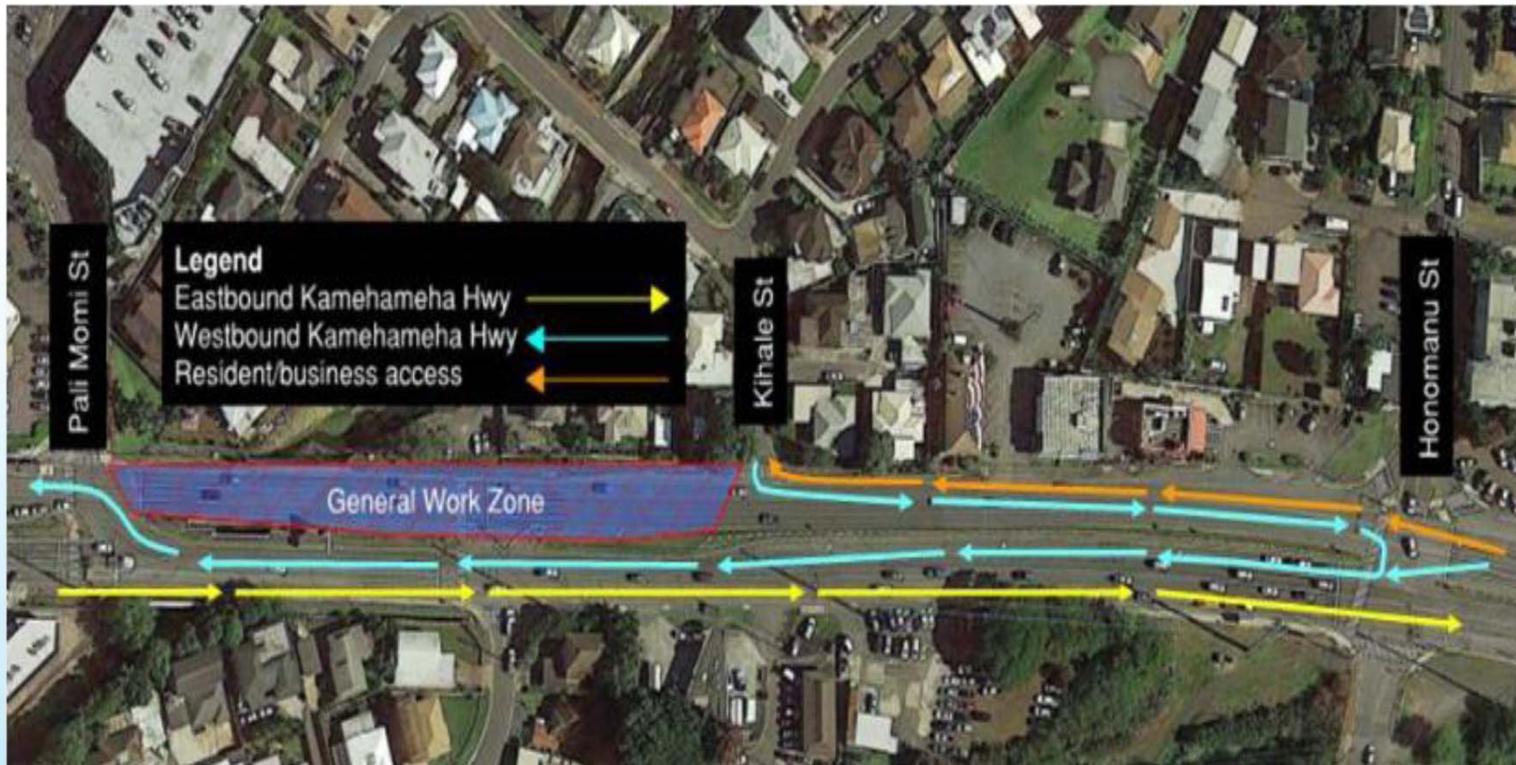

Kamehameha Highway in Aiea

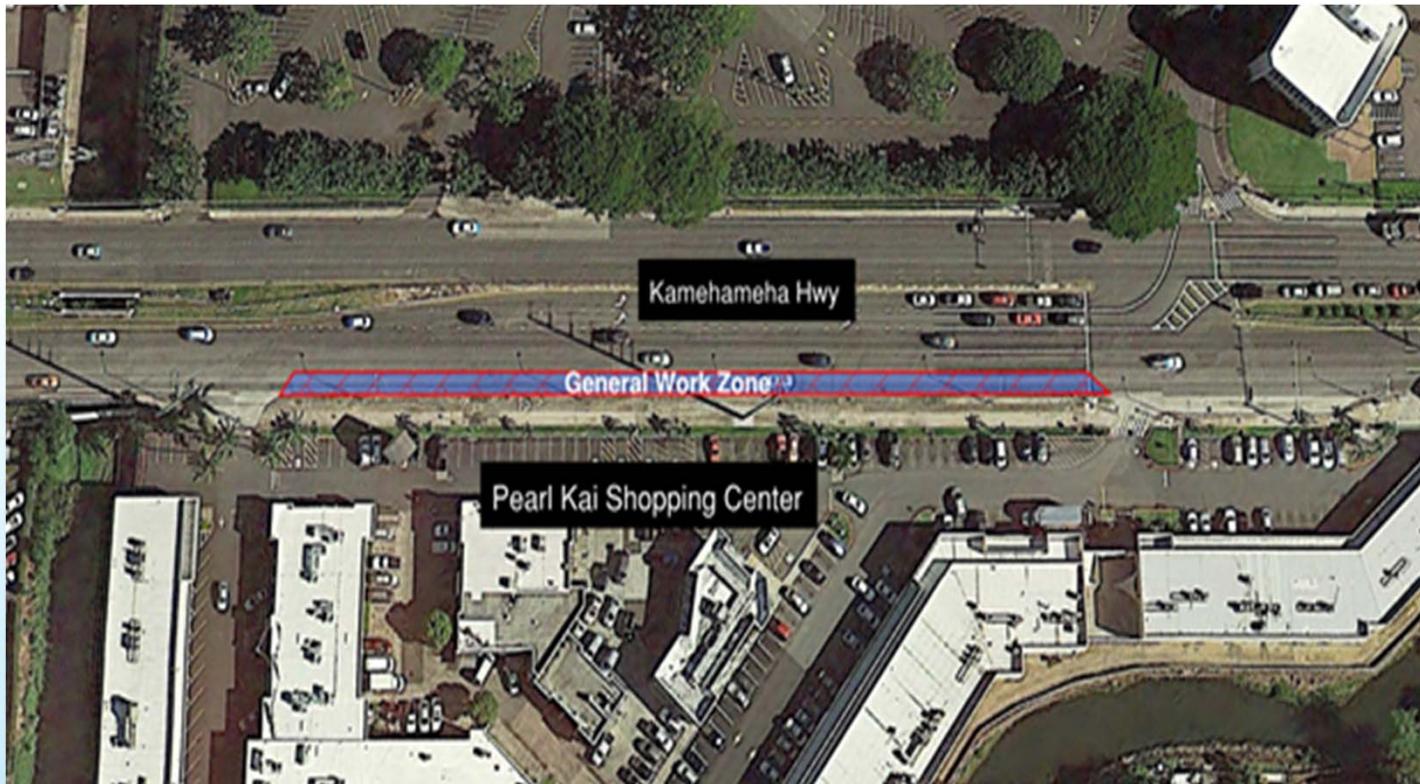

Kamehameha Highway near Pearl Harbor

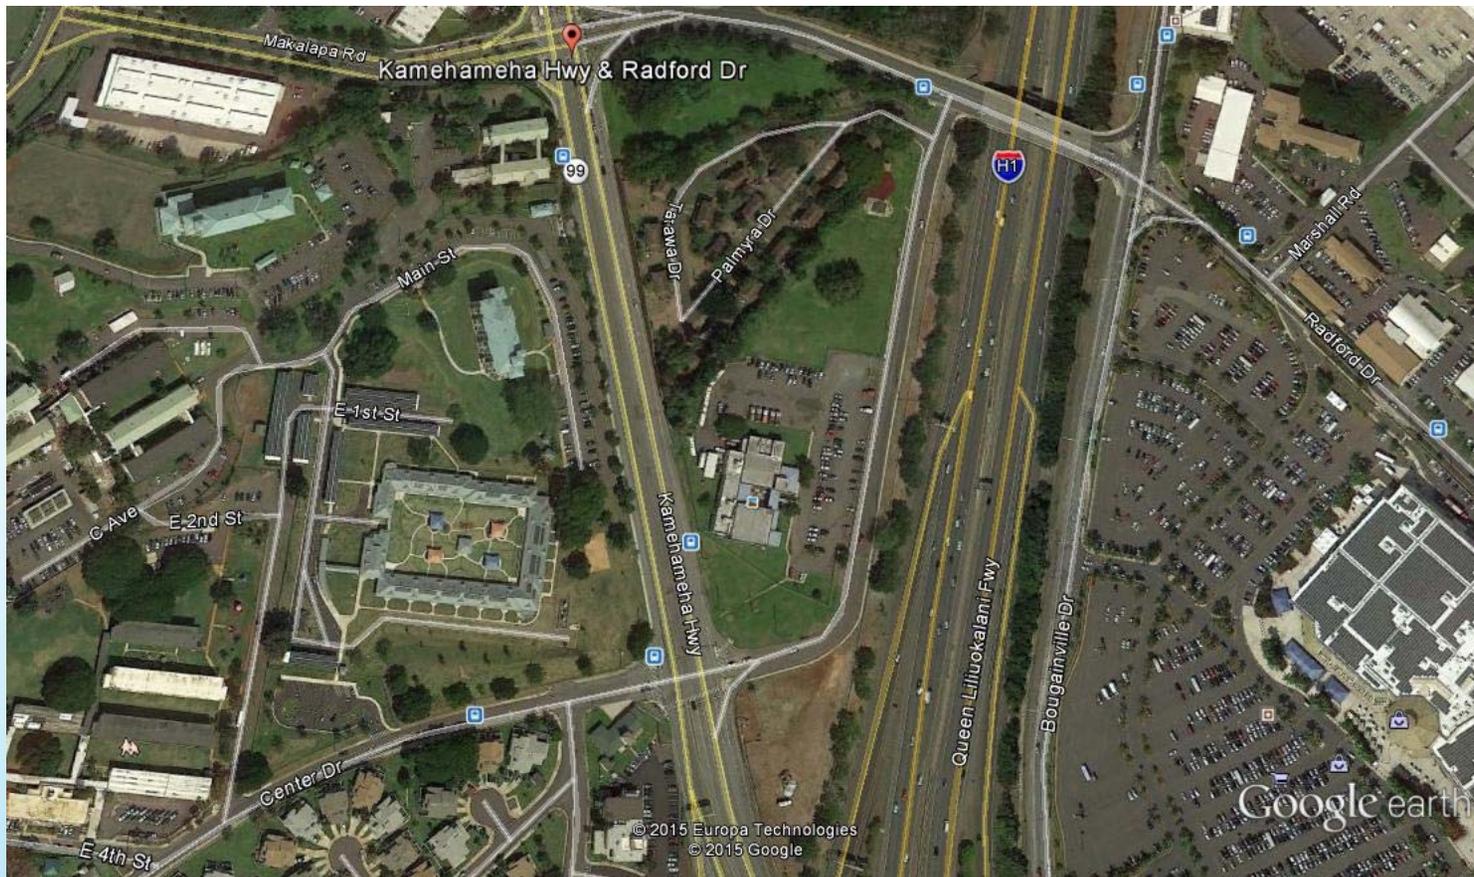

Mahalo!



HONOLULU RAIL TRANSIT

H O N O L U L U R A I L T R A N S I T P R O J E C T

www.HONOLULUTRANSIT.ORG

HART

HONOLULU AUTHORITY for RAPID TRANSPORTATION
