


## Weekly AIS Update – City Center April 30, 2012 through May 6, 2012

Trench #	Date Excavated	TMK	LCA	Results
74	4/30/2012	N/A	11056	No iwi kūpuna and/or human skeletal remains were found.
19	5/2/2012	N/A	50:3	No iwi kūpuna and/or human skeletal remains were found.
78	5/2/2012	N/A	8504:3	No iwi kūpuna and/or human skeletal remains were found.
20	5/4/2012	N/A	N/A	No iwi kūpuna and/or human skeletal remains were found.
95	5/5/2012	[1] 1-15-080:020	N/A	No iwi kūpuna and/or human skeletal remains were found.


### Archaeological Inventory Survey Fieldwork

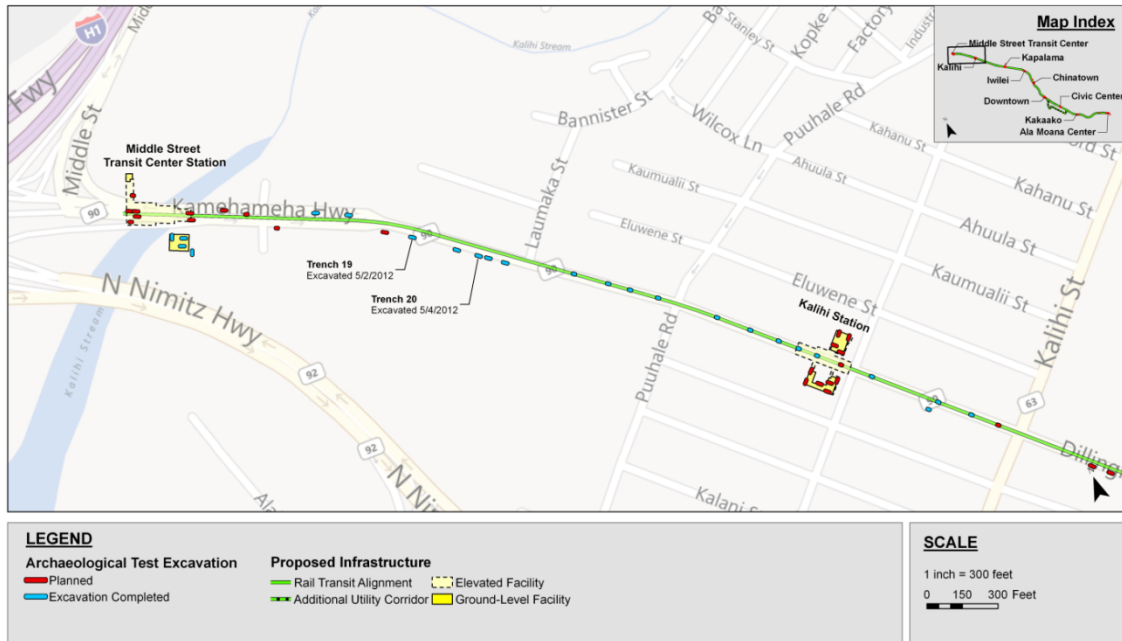

Honolulu High-Capacity Transit Corridor Project - City Center Section

Archaeological Test Excavation Progress Map, May 2012

### Archaeological Inventory Survey Fieldwork

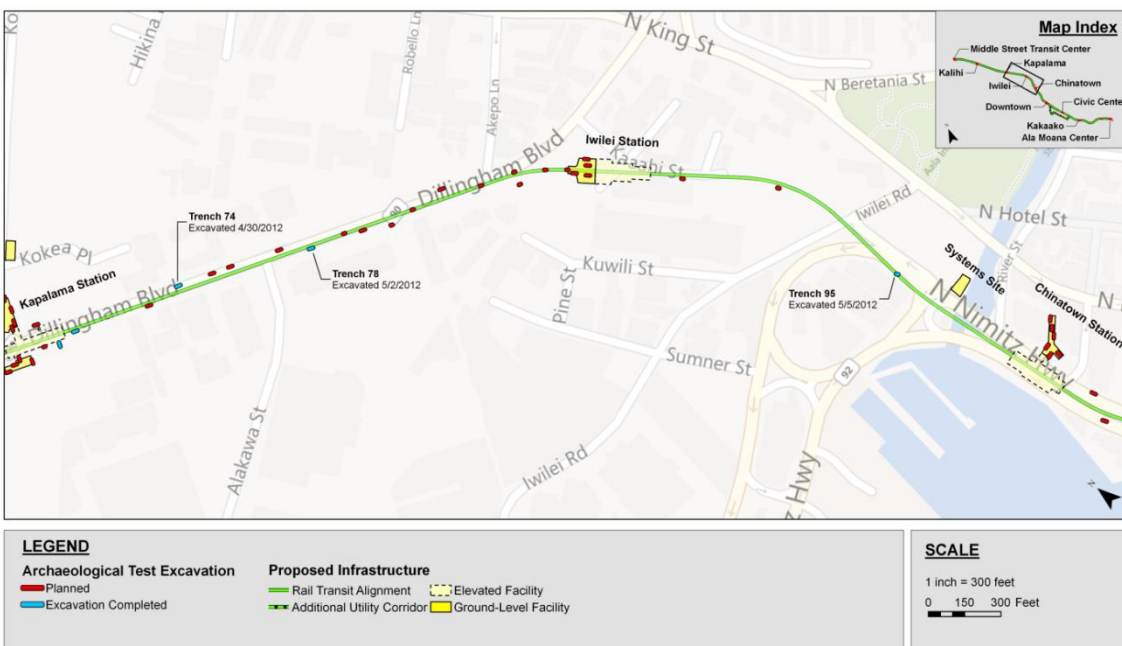



Honolulu High-Capacity Transit Corridor Project - City Center Section

Archaeological Test Excavation Progress Map, May 2012

## Outreach & Consultation

- Website & social media posts of City Center AIS Traffic Update on 4/29 for the week of April 29 – May 5 to [www.HonoluluTransit.org](http://www.HonoluluTransit.org).



**CITY CENTER** 

**City Center AIS Field Work Traffic Update | Week of April 29, 2012**

The Honolulu Authority for Rapid Transportation (HART) wants to inform drivers that archaeological survey work continues next week in the urban Honolulu area for the rail transit project.

Motorists are advised of lane closures related to the survey work being conducted in the Kalihi, downtown Honolulu, and Kaka'ako areas.

Work will require lane closures during non-peak traffic hours, including possible night work in approved areas. For the safety of both the work crews and motorists, the public is advised to proceed with caution through these areas. Drivers should anticipate possible traffic delays or use alternate routes during work hours.

Work for the week of Monday, April 30 will take place at the following locations:

- Kamehameha Highway (in Kalihi) between Middle Street and Laumaka Street from 8:30 a.m. to 3 p.m. and from 7:30 p.m. to 3 a.m.
- Dillingham Boulevard between Puuhale Road and Kalihi Street from 8:30 a.m. to 3 p.m.
- Dillingham Boulevard between Kokea Street and Kaaahi Street from 7 p.m. to 3 a.m.

Motorists are advised to drive with caution and provide a safe distance between themselves and the construction workers and vehicles.

The City is conducting the archaeological survey work along the urban Honolulu section of the Honolulu rail transit route to identify potential archaeological, historical and cultural resources. The archaeological work will aid rail project staff in their design of the elevated rail guideway.

Trenching work will take place at various locations along the Honolulu rail route between Middle Street in Kalihi and Ala Moana Center. Contractors Cultural Surveys Hawaii Inc. and Royal Contracting Co. are conducting the fieldwork.

The survey work will be completed before rail construction begins in the urban Honolulu area, as specified under the rail project's programmatic agreement relating to cultural and historic resources.

- Media Advisory Traffic Update distributed to local media on 4/27 for the week of April 29 – May 5 to [www.HonoluluTransit.org](http://www.HonoluluTransit.org).

*Note: Traffic announcement weeks start on a Sunday and end on Saturday.*
