
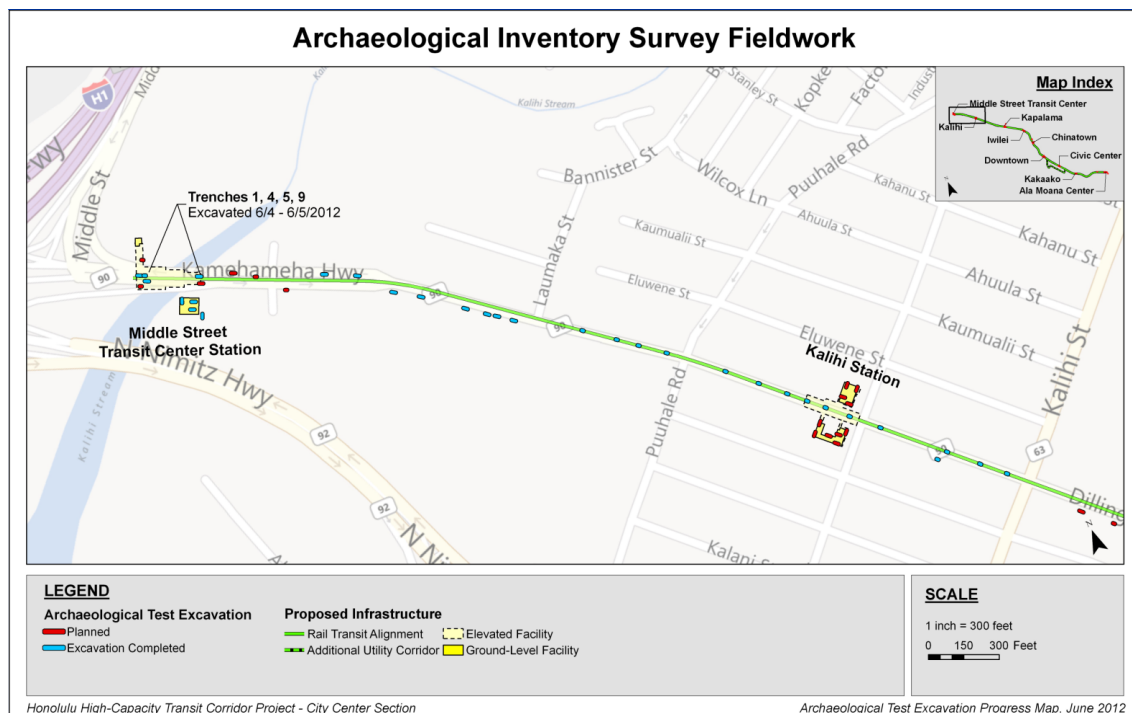


Weekly AIS Update – City Center June 3, 2012 through June 9, 2012

Trench #	Date Excavated	TMK	LCA	Results
93	6/4/2012	1-5-007:026, 028	N/A	No iwi kūpuna and/or human skeletal remains were found
1	6/4/2012	1-2-013	818 Part 6:12	No iwi kūpuna and/or human skeletal remains were found
4	6/5/2012	1-2-013	818 Part 6:12	No iwi kūpuna and/or human skeletal remains were found
5	6/5/2012	1-2-013	818 Part 6:12	No iwi kūpuna and/or human skeletal remains were found
9	6/4/2012	1-2-013	818 Part 6:12	No iwi kūpuna and/or human skeletal remains were found

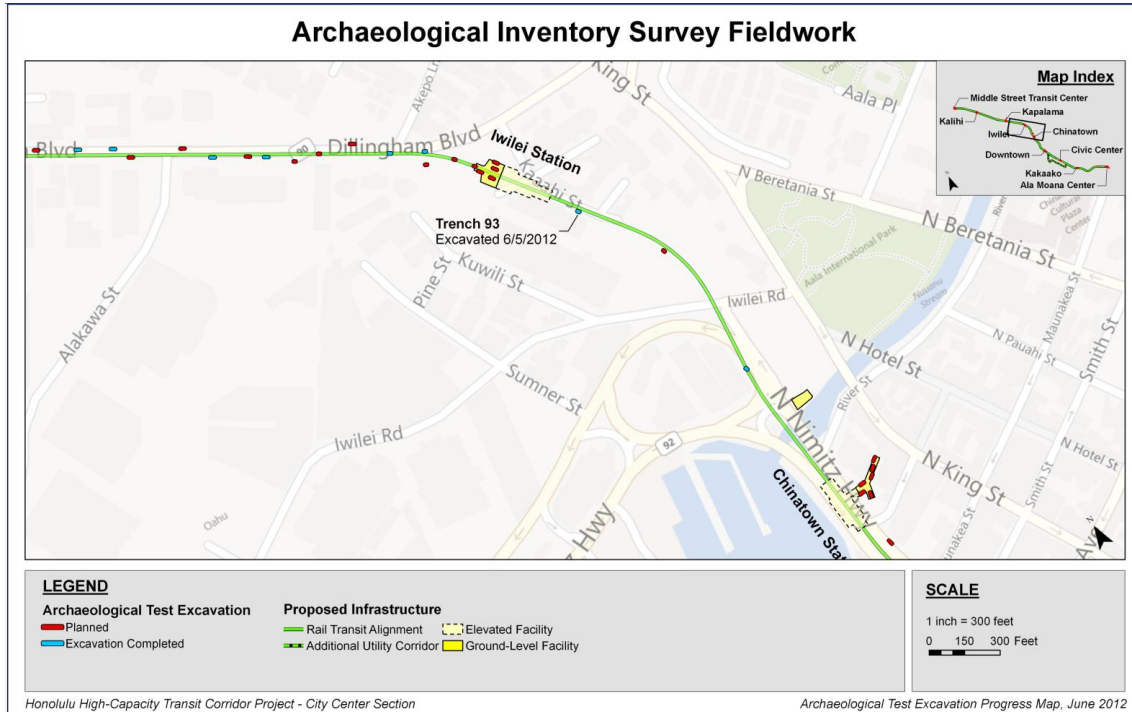

Outreach & Consultation

- Website and social media posts of Airport Traffic Update on 6/3 for the week of June 3 – 9 to www.HonoluluTransit.org.



City Center AIS Field Work Traffic Update | Week of Jun. 3, 2012

The Honolulu Authority for Rapid Transportation (HART) wants to inform drivers that archaeological survey work continues next week in the urban Honolulu area for the rail transit project.

Motorists are advised of lane closures related to the survey work being conducted in the Kalihi, downtown Honolulu, and Kaka'ako areas.

Work will require lane closures during non-peak traffic hours, including possible night work in approved areas.

For the safety of both the work crews and motorists, the public is advised to proceed with caution through these areas. Drivers should anticipate possible traffic delays or use alternate routes during work hours, and provide a safe distance between themselves and the construction workers and equipment.

Work for the week of Sunday, June 3, through Saturday, June 9, will take place at the following locations:

- Dillingham Boulevard between McNeill Street and Akepo Lane from 8:30 a.m. to 3 p.m.
- Nimitz Highway between River Street and Halekauwila Street from 8:30 a.m. to 3 p.m.
- Kaaahi Street between Kaaahi Place and Kaamahu Place from 8:30 a.m. to 3 p.m.
- Kamehameha Highway between Middle Street and Laumaka Street from 7:30 p.m. to 4 a.m.

The City is conducting the archaeological survey work along the urban Honolulu section of the Honolulu rail transit route to identify potential archaeological, historical and cultural resources. The archaeological work will aid rail project staff in their design of the elevated rail guideway.

Trenching work will take place at various locations along the Honolulu rail route between Middle Street in Kalihi and Ala Moana Center. Contractors Cultural Surveys Hawaii Inc. and Royal Contracting Co. are conducting the fieldwork.

The survey work will be completed before rail construction begins in the urban Honolulu area, as specified under the rail project's programmatic agreement relating to cultural and historic resources.

- Media Advisory Traffic Update distributed to local media on 6/1 for June 3 – 9.
- Notice to Motorists ad in the Honolulu Star-Advertiser on 6/4 for June 4 – 16.

Notices to Motorists

NOTICE TO MOTORISTS

The Honolulu Authority for Rapid Transportation has begun work on an Archaeological Inventory Survey of the City Center section for the Honolulu Rail Transit Project. Work continues to commence during the week of June 4, 2012 and will require lane and mobile lane closures during non-peak traffic hours, including night work in approved areas. Work will be performed in the following areas:

- Dillingham Blvd. from Middle St. to Kaaahi St./Kaamahu Pl. between 8:30am and 3:30pm or 8:00pm and 4:00am
- Kamehameha Highway from Middle St. to Laumaka St. between 9:00am and 3:00pm or 8:00pm and 4:00am
- Nimitz Highway from River St. to Halekauwila St. between 9:00am and 3:00pm or 8:00pm and 4:00am

The public will be notified of detours and change of access via traffic control signs. Special duty police officers will be used when needed to direct traffic at affected areas. Motorists are advised to anticipate possible traffic delays or use alternate routes.

For more information and updated work schedules, call the project's 24-hour hotline at (808) 566-2299 or visit www.HonoluluTransit.org. (SA421436 6/4/12)

Note: Traffic announcement weeks start on a Sunday and end on Saturday.
