


Weekly AIS Update – City Center September 30, 2012 through October 6, 2012

| Trench # | Date Excavated | TMK | LCA | Results |
|----------|----------------|----------------------|--------------|--|
| 60 | 9/30/2012 | 1-5-020: 003 | N/A | No iwi kūpuna and/or human skeletal remains were found |
| 61 | 9/30/2012 | 1-5-020: 003 | N/A | No iwi kūpuna and/or human skeletal remains were found |
| 63 | 9/30/2012 | 1-5-020: 003 | 275 B | No iwi kūpuna and/or human skeletal remains were found |
| 68 | 9/30/2012 | 1-5-020: 003 | 275 B | No iwi kūpuna and/or human skeletal remains were found |
| 103 | 9/30/2012 | Nimitz Hwy. ROW | N/A | No iwi kūpuna and/or human skeletal remains were found |
| 111 | 9/30/2012 | Nimitz Hwy. ROW | N/A | No iwi kūpuna and/or human skeletal remains were found |
| 107 | 10/1/2012 | Nimitz Hwy. ROW | N/A | No iwi kūpuna and/or human skeletal remains were found |
| 109 | 10/1/2012 | Nimitz Hwy. ROW | N/A | No iwi kūpuna and/or human skeletal remains were found |
| 105 | 10/2/2012 | Nimitz Hwy. ROW | N/A | No iwi kūpuna and/or human skeletal remains were found |
| 106 | 10/2/2012 | Nimitz Hwy. ROW | N/A | No iwi kūpuna and/or human skeletal remains were found |
| 110 | 10/3/2012 | Nimitz Hwy. ROW | N/A | No iwi kūpuna and/or human skeletal remains were found |
| 184 | 10/3/2012 | Waimanu St. ROW | N/A | No iwi kūpuna and/or human skeletal remains were found |
| 50 | 10/4/2012 | Dillingham Blvd. ROW | N/A | No iwi kūpuna and/or human skeletal remains were found |
| 51 | 10/4/2012 | Dillingham Blvd. ROW | N/A | No iwi kūpuna and/or human skeletal remains were found |
| 108 | 10/4/2012 | Nimitz Hwy. ROW | N/A | Faunal remains documented within a historic fill layer |
| 141 | 10/6/2012 | Halekauwila St. ROW | 982 / 7712:6 | Subsurface cultural deposit. Disarticulated human remains from at least two separate individuals |
| 142 | 10/6/2012 | Halekauwila St. ROW | 982 | Subsurface cultural deposit. Single, intact human burial. |



Archaeological Inventory Survey Fieldwork

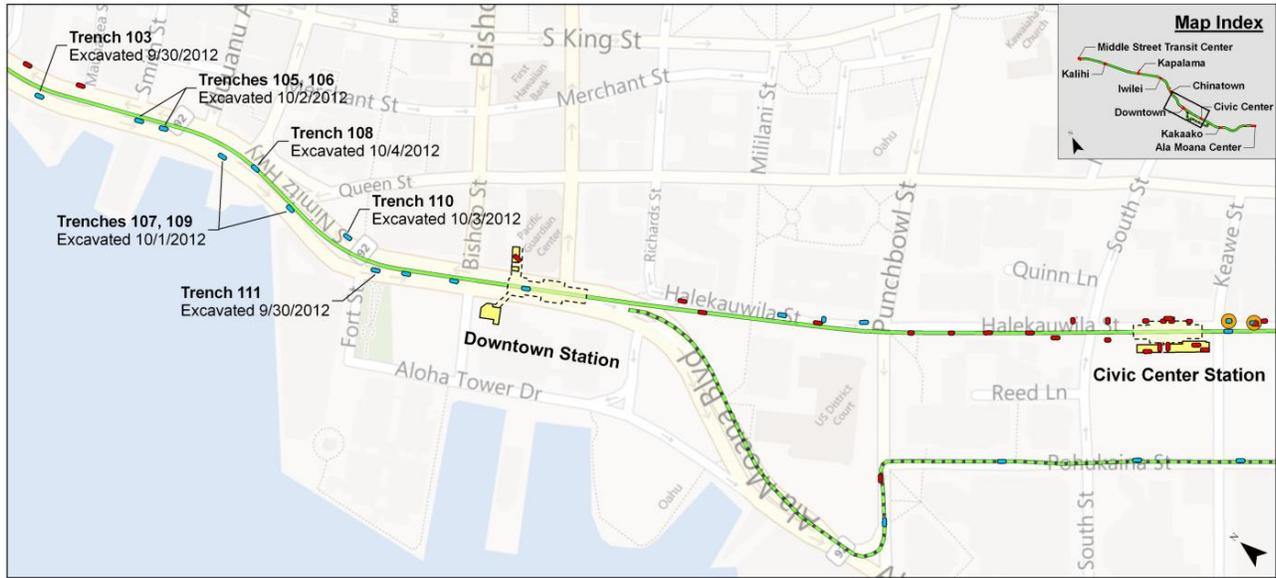

LEGEND

Archaeological Test Excavation
 ● Planned
 ● Excavation Completed

Cultural Resource
 ● Subsurface Cultural Deposit
 ▲ Burial Site

Proposed Infrastructure
 — Rail Transit Alignment
 — Additional Utility Corridor
 □ Elevated Facility
 □ Ground-Level Facility


SCALE

1 inch = 300 feet
 0 150 300 Feet

Honolulu High-Capacity Transit Corridor Project - City Center Section

Archaeological Test Excavation Progress Map, October 2012

Archaeological Inventory Survey Fieldwork

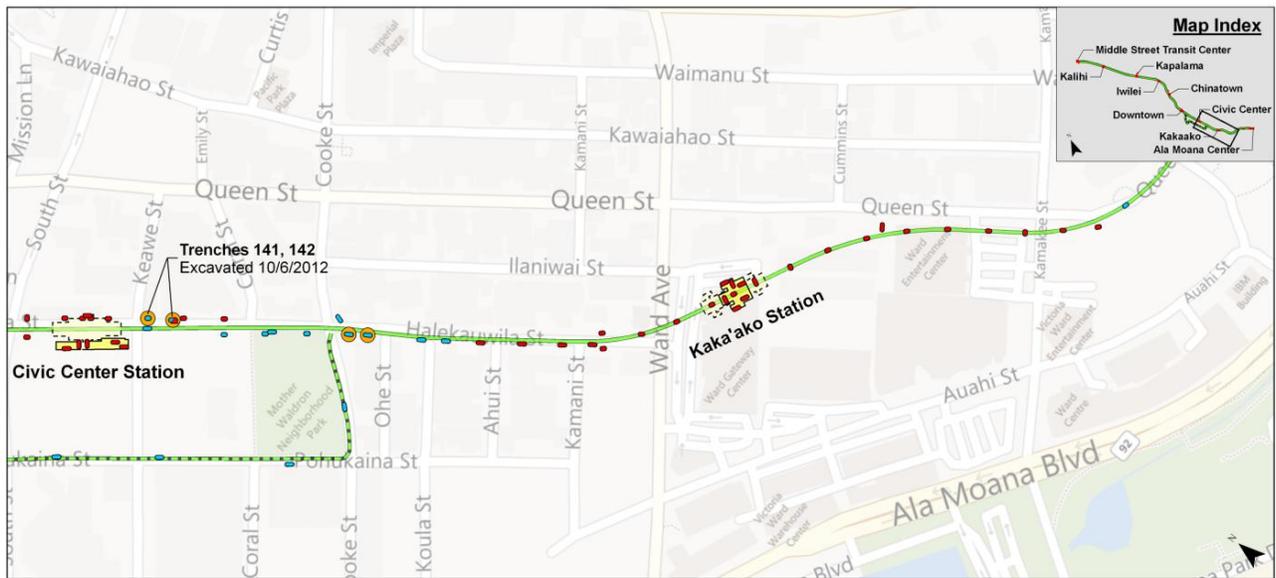

LEGEND

Archaeological Test Excavation
 ● Planned
 ● Excavation Completed

Cultural Resource
 ● Subsurface Cultural Deposit
 ▲ Burial Site

Proposed Infrastructure
 — Rail Transit Alignment
 — Additional Utility Corridor
 □ Elevated Facility
 □ Ground-Level Facility


SCALE

1 inch = 300 feet
 0 150 300 Feet

Honolulu High-Capacity Transit Corridor Project - City Center Section

Archaeological Test Excavation Progress Map, October 2012

Archaeological Inventory Survey Fieldwork

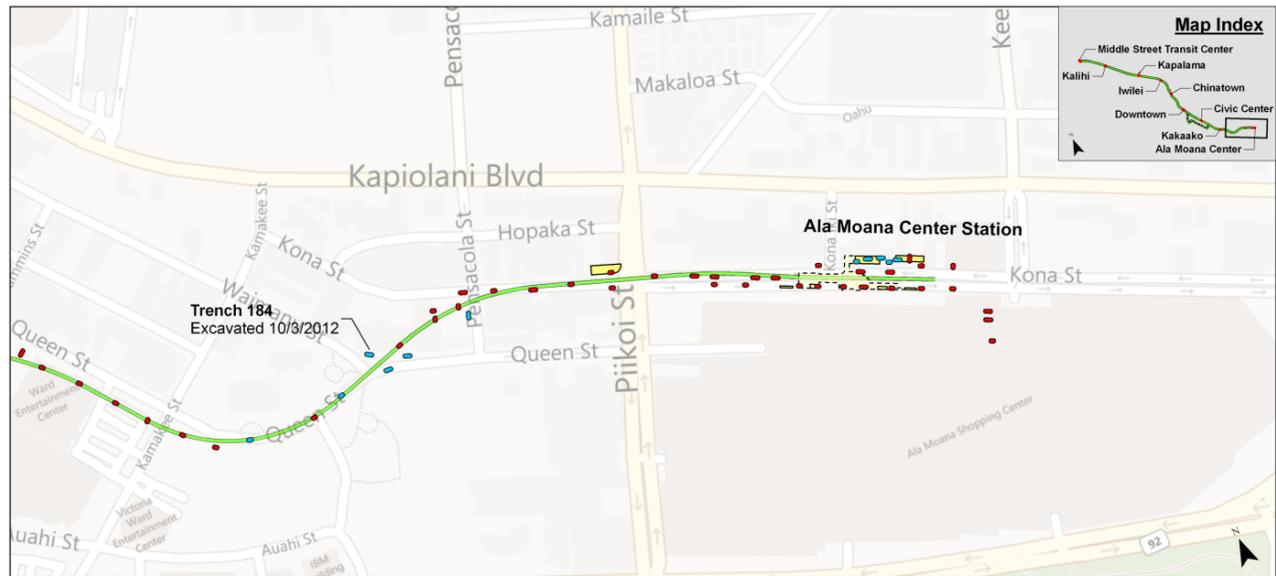

Honolulu High-Capacity Transit Corridor Project - City Center Section

Archaeological Test Excavation Progress Map, October 2012

Outreach & Consultation

- Website and social media posts of City Center Traffic Update on 9/28 for the week of September 30 – October 6 to www.HonoluluTransit.org.



City Center AIS Field Work Traffic Update | Week of Sept. 30, 2012

The Honolulu Authority for Rapid Transportation (HART) wants to inform drivers that archaeological survey work continues next week in the urban Honolulu area for the rail transit project.

Motorists are advised of lane closures related to the survey work being conducted in the Kaka'ako area. Work will require lane closures during non-peak traffic hours.

For the safety of both the work crews and motorists, the public is advised to proceed with caution through these areas. Drivers should anticipate possible traffic delays or use alternate routes during work hours, and provide a safe distance between themselves and the construction workers and equipment.

Work for the week of Sunday, September 30, through Saturday, October 6, will take place at the following locations between the hours of 8:30 a.m. and 3 p.m., unless otherwise noted.

- Ala Onaona Street between Ala 'Auana Street and Aolele Street
- Waimanu Street between Waimanu Street and Pensacola Street
- Halekauwila Street between Keawe Street and Cooke Street
- Nimitz Highway between Kekaulike Street and Aloha Tower Drive/Fort Street Mall (some work will also take place from 7:30 p.m. to 3:30 a.m.)

The City is conducting the archaeological survey work along the urban Honolulu section of the Honolulu rail transit route to identify potential archaeological, historical and cultural resources. The archaeological work will aid rail project staff in their design of the elevated rail guideway.

Contractors Cultural Surveys Hawaii Inc. and Royal Contracting Co. are conducting the fieldwork.

The survey work will be completed before rail construction begins in the urban Honolulu area, as specified under the rail project's programmatic agreement relating to cultural and historic resources.

- Media Advisory Traffic Update distributed to local media on 10/1 for the week of October 1 – 6.

- Notice to Motorists ad in the Honolulu Star-Advertiser on 10/1 for September 30 – October 13.

NOTICE TO MOTORISTS

The Honolulu Authority for Rapid Transportation continues with the Archaeological Inventory Survey in the Airport and City Center sections of the Honolulu Rail Transit Project. Work continues between September 30, 2012 through October 13, 2012 and will require mobile lane closures during non-peak traffic hours. Work will be performed in the following areas between the hours of 8:30am and 3:30pm, unless otherwise noted below:

- Ala Onaona St. between Ala 'Auana St. and Aolele St.
- Waimanu St. between Waimanu St. and Pensacola St.
- Halekauwila St. between Punchbowl St. and Coral St.
- Dillingham Blvd. between Kokea St. and Alakawa St.
- Kamehameha Hwy. between Arizona Memorial Pl./Kalaloa St. and Arizona St./Halawa Dr.
- Nimitz Hwy. between Kekaulike St. and Aloha Tower Dr./Fort Street Mall (or 7:30pm - 3:30am)
- Kamehameha Hwy. between Middle St. and Laumaka St. (or 7:30pm - 3:30am)
- Dillingham Blvd. between Alakawa St. and Akepo Ln. (or 7:30pm - 3:30am)

The public will be notified of detours and change of access via traffic control signs. Special duty police officers will be used when needed to direct traffic at affected areas. Motorists are advised to anticipate possible traffic delays or use alternate routes.

For more information and updated work schedules, call the project's 24-hour hotline at (808) 566-2299 or visit www.HonoluluTransit.org.
(SA456984 10/1/12)

Note: Traffic announcement weeks start on Sunday and end on Saturday.
