



Weekly AIS Update – City Center November 4, 2012 through November 10, 2012

Trench #	Date Excavated	TMK	LCA	Results
116	11/4/2012	Halekauwila St. ROW	N/A	Faunal remains documented within a historic fill layer
120	11/4/2012	Halekauwila St. ROW	N/A	Subsurface cultural deposit.
98	11/5/2012	1-7-002: 026	170	Subsurface historic architectural remnants.
100	11/5/2012	1-7-002: 026	170	Faunal remains documented within a historic fill layer. Subsurface historic architectural remnants.
99	11/6/2012	1-7-002: 026	170	Subsurface historic architectural remnants.
101	11/6/2012	1-7-002: 026	170	Faunal remains documented within a historic fill layer. Subsurface historic architectural remnants.
154	11/7/2012	2-1-052: 022	387	No iwi kūpuna and/or human skeletal remains were found
155	11/7/2012	2-1-052: 022	387	No iwi kūpuna and/or human skeletal remains were found
162	11/8/2012	2-3-002: 059	387	No iwi kūpuna and/or human skeletal remains were found
163	11/8/2012	2-3-002: 059	387	No iwi kūpuna and/or human skeletal remains were found
165	11/8/2012	2-3-002: 059	387	No iwi kūpuna and/or human skeletal remains were found
164	11/9/2012	2-3-002: 059	387	No iwi kūpuna and/or human skeletal remains were found
166	11/9/2012	2-3-002: 059	387 <td No iwi kūpuna and/or human skeletal remains were found	
167	11/9/2012	2-3-002: 059	387	Subsurface cultural deposit.

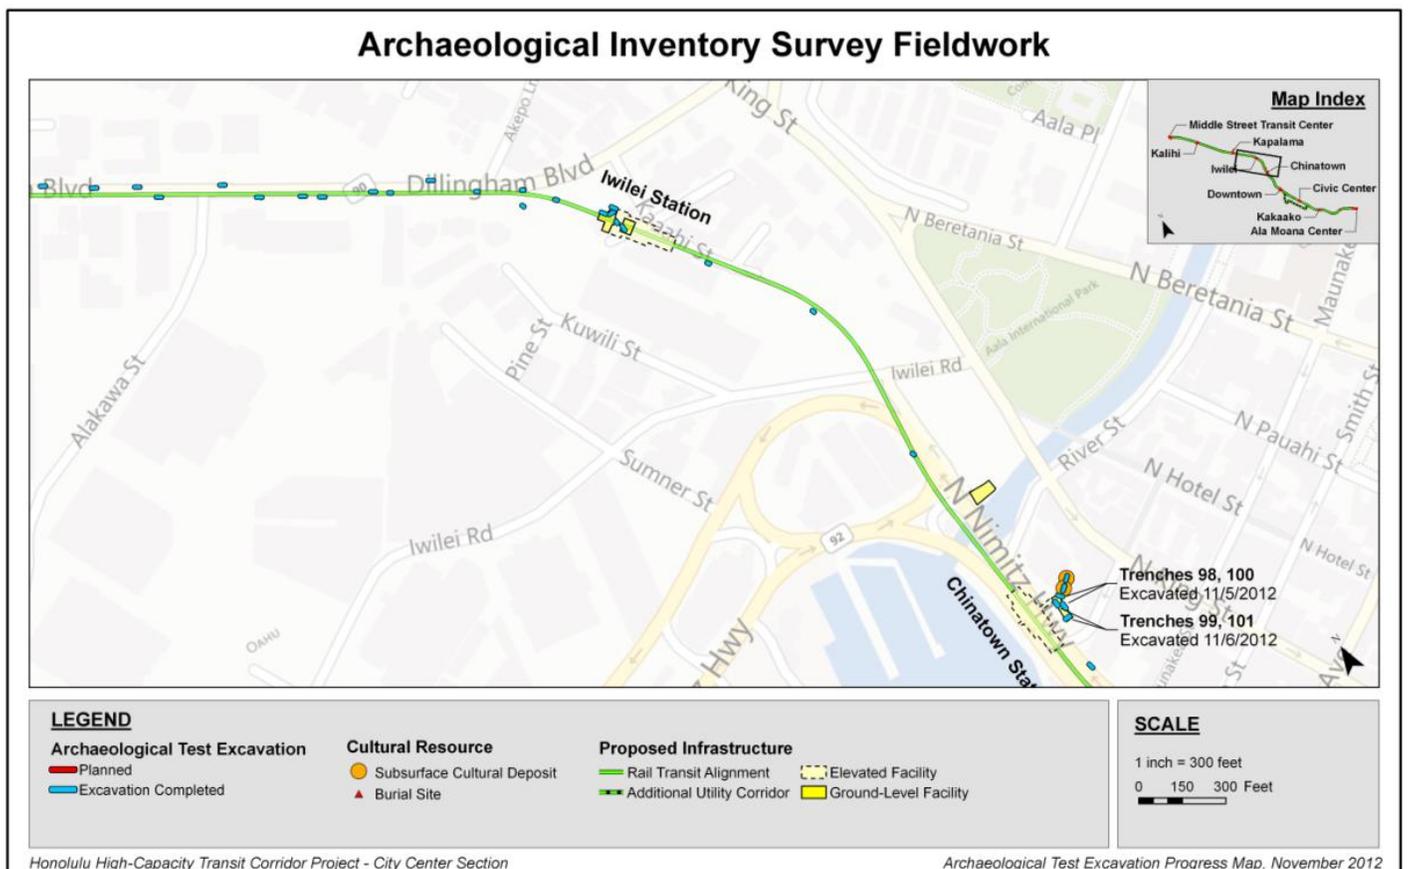

Archaeological Inventory Survey Fieldwork

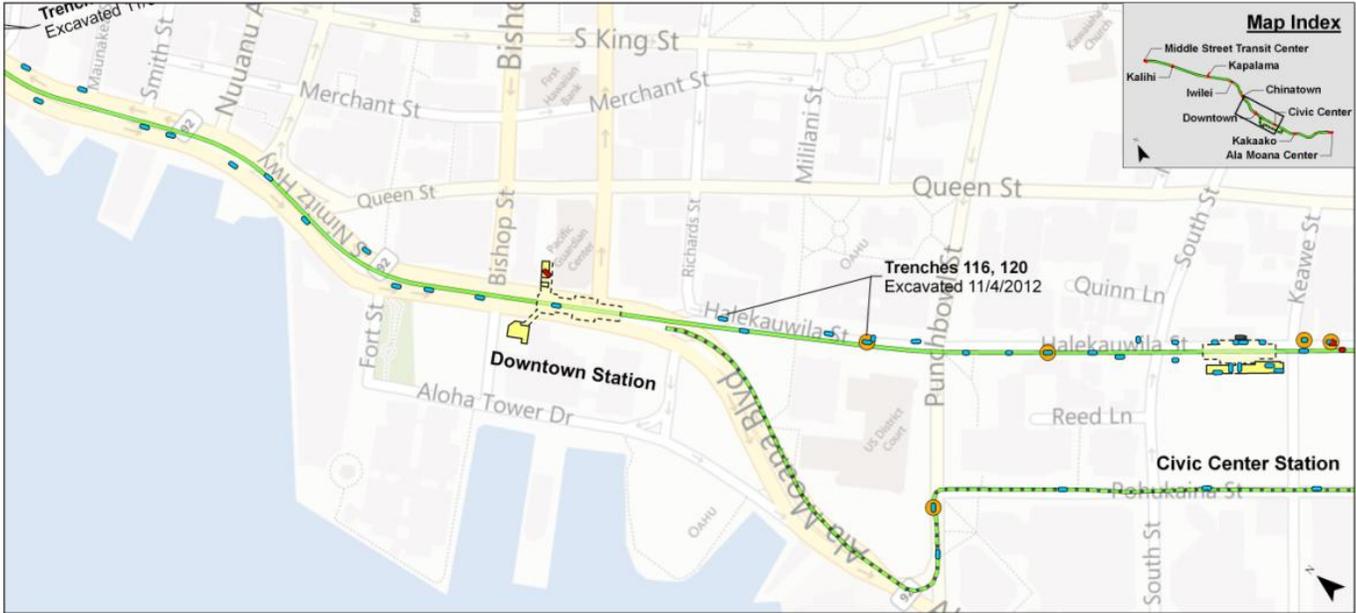

LEGEND

Archaeological Test Excavation
— Planned
— Excavation Completed


Cultural Resource
● Subsurface Cultural Deposit
▲ Burial Site

Proposed Infrastructure
— Rail Transit Alignment
— Additional Utility Corridor
 Elevated Facility
 Ground-Level Facility

SCALE

1 inch = 300 feet
 0 150 300 Feet

Archaeological Inventory Survey Fieldwork

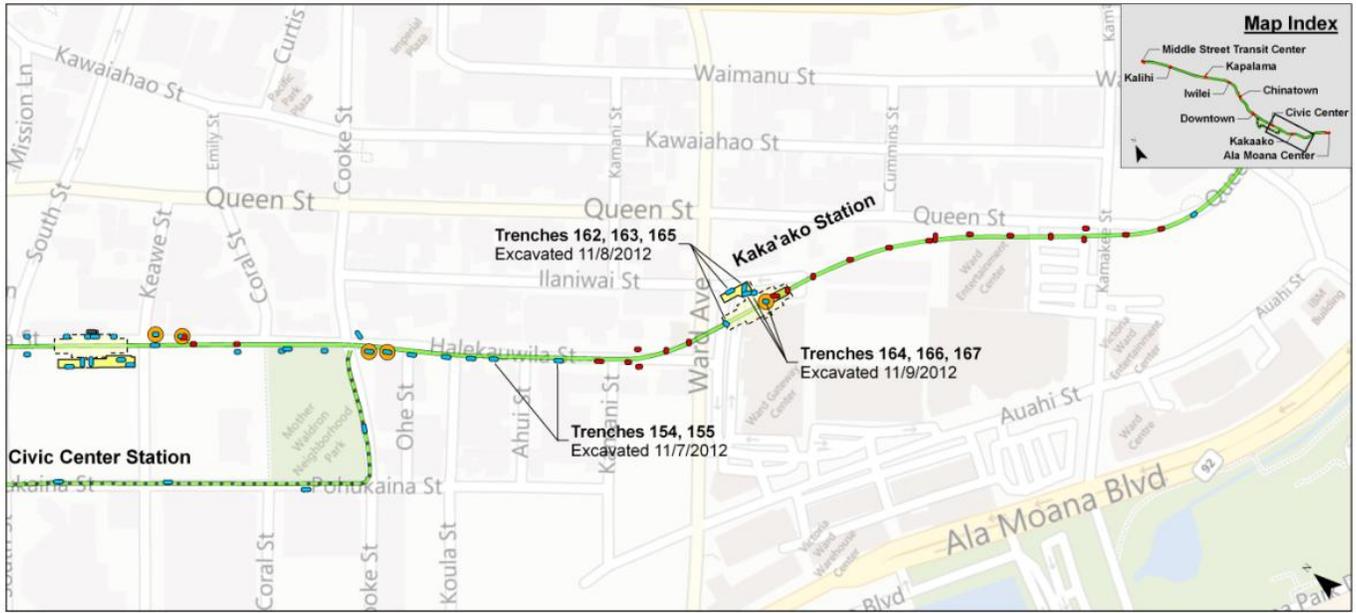

LEGEND

Archaeological Test Excavation
— Planned
— Excavation Completed

Cultural Resource
● Subsurface Cultural Deposit
▲ Burial Site

Proposed Infrastructure
— Rail Transit Alignment
— Additional Utility Corridor
 Elevated Facility
 Ground-Level Facility

SCALE

1 inch = 300 feet
 0 150 300 Feet

Outreach & Consultation

- Website and social media posts of City Center Traffic Update on 11/4 for the week of November 4 – 10 to www.HonoluluTransit.org.

CITY CENTER < |||

City Center AIS Field Work Traffic Update | Week of Nov. 4, 2012

The Honolulu Authority for Rapid Transportation (HART) wants to inform drivers that archaeological survey work continues next week in the urban Honolulu area for the rail transit project.

Motorists are advised of lane closures related to the survey work being conducted. Work will require lane closures during non-peak traffic hours.

For the safety of both the work crews and motorists, the public is advised to proceed with caution through these areas. Drivers should anticipate possible traffic delays or use alternate routes during work hours, and provide a safe distance between themselves and the construction workers and equipment.

Work for the week of Sunday, November 4, through Saturday, November 10, will take place at the following locations between the hours of 8:30 a.m. and 3:30 p.m.:

- Halekauwila Street between Richards Street and Punchbowl Street

The City is conducting the archaeological survey work along the urban Honolulu section of the Honolulu rail transit route to identify potential archaeological, historical and cultural resources. The archaeological work will aid rail project staff in their design of the elevated rail guideway.

Contractors Cultural Surveys Hawaii Inc. and Royal Contracting Co. are conducting the fieldwork.

The survey work will be completed before rail construction begins in the urban Honolulu area, as specified under the rail project's programmatic agreement relating to cultural and historic resources.

- Media Advisory Traffic Update distributed to local media on 11/2 for the week of November 4 – 10.

Note: Traffic announcement weeks start on Sunday and end on Saturday.
