



HART Board
Construction and Traffic Update
for September 29, 2016

West Oahu-Farrington Guideway, (Kapolei to Pearl Highlands), Kiewit Infrastructure West Co.

- 96% complete
- Projected Contract Completion: March 2017

West Oahu Stations Group (East Kapolei, UH West Oahu and Ho'opili), Nan Inc.

- 5% complete
- Contract Completion: March 2018
- UH West Oahu BMP issues with HDOT have been resolved, 3rd shaft drilled and cage is in place.
- 2 days rained out; Ho'opili TCCR and UH West Oahu entry building was impacted.
- Ho'opili Platform girder concrete reinforcement being placed, including sleeves and imbeds

Farrington Highway Stations Group (West Loch, Waipahu Transit Center and LCC), Hawaiian Dredging Construction Co.

- 1% complete (36% behind schedule) Contract Start: (Notice To Proceed) Aug 2015
- Contract Completion: Jan 2018
- West Loch – Makai side drilled shafts complete; installed underground utilities in the bus driveway; installed grounding grid at the Ancillary building; installing conduit in slab at Ancillary building
- Waipahu Transit Center– Survey control points installed
- LCC – No HDCC work; Kiewit work continues

Maintenance and Storage Facility, Kiewit-Kobayashi Joint Venture

- Substantial Completion issued July 2, 2016
- Anticipated Final Acceptance Date is December 1, 2016
- MSF Punch list Items – 98.3% (47 more items to be completed)

H2R2 Ramp, Royal Contracting Co.

- 25.2% complete
- Contract Completion: May 2016 Projected Completion: May 2017
- Surcharge settlement monitoring continues.

Pearl Highlands Transit Center and Parking Garage

- Solicitation in preparation

Kam Highway Guideway (Pearl Highlands to Stadium), Kiewit Infrastructure West Co.

- 77.3% complete
- Contract Completion: May 2017

Kam Highway Stations Group (Pearl Highlands, Pearlridge and Aloha Stadium), Nan Inc.

- 0% complete Notice To Proceed: Planned issuance for October 3, 2016 (32 month contract)
- Nan to obtain full access to Pearl Highlands and Pearlridge sites in October 2016. Discussions are ongoing regarding shared access at the Aloha Stadium Station site.

Airport Utilities Construction, Nan Inc.

- 60.3% complete, phase out in progress with work transition to airport guideway and stations design-build contract
- Contract Completion: Jul 2016 Projected Completion: Nov 2016

Airport Guideway and Stations (Aloha Stadium to Middle Street)

- Contract award to Shimmick, Traylor and Granite (STG) in progress
- NTP projected Oct/Nov 2016

Core Systems, Ansaldo Honolulu Joint Venture


- 34% complete – Vehicles and Core Systems
- Contract Completion: Mar 2019 Projected Completion: Jul 2024
- MSF activities 53% complete with anticipated completion of all TPSS and Signaling work by the end of the year.
- Train 2 is 83% complete and continues Water Testing and Initial Static Testing.

Farrington Highway in Waipahu




- Various daytime and nighttime closures between Old Fort Weaver Road and Kahualii Street for finishing and traffic signal work through November 2016

H-1 in Pearl City

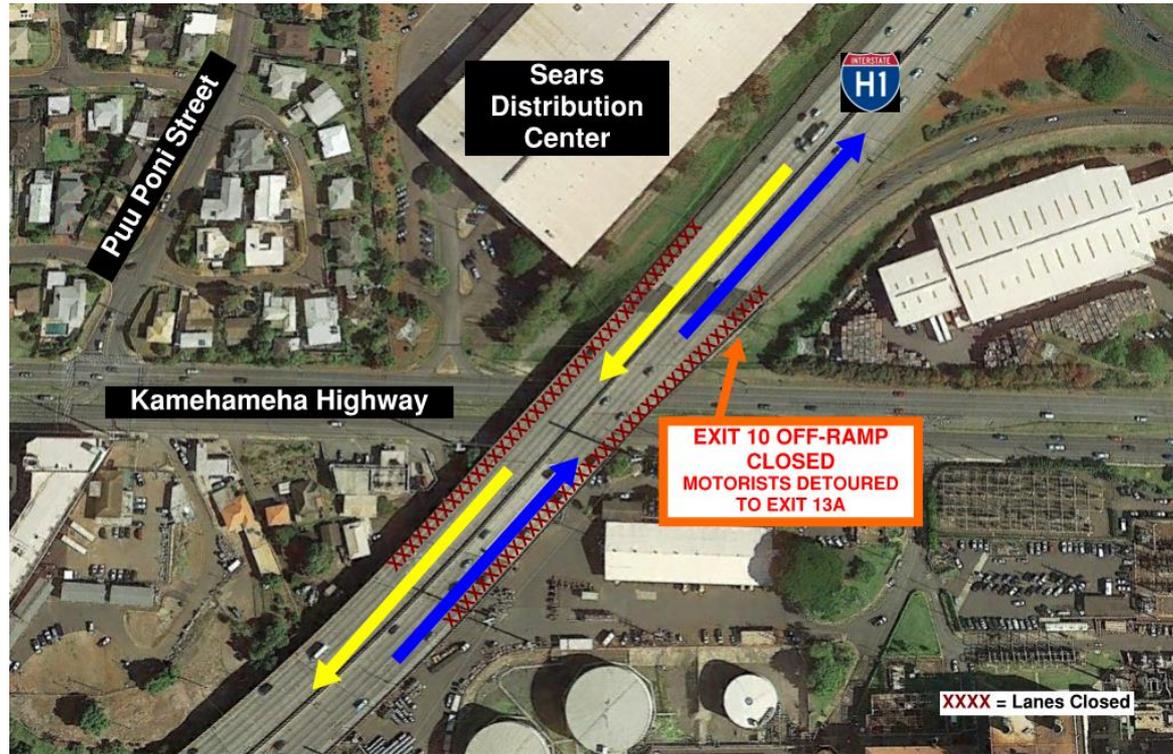


- Standard nightly closures on eastbound and westbound H-1 in Pearl City through November 2016

Kamehameha Highway in Pearl City

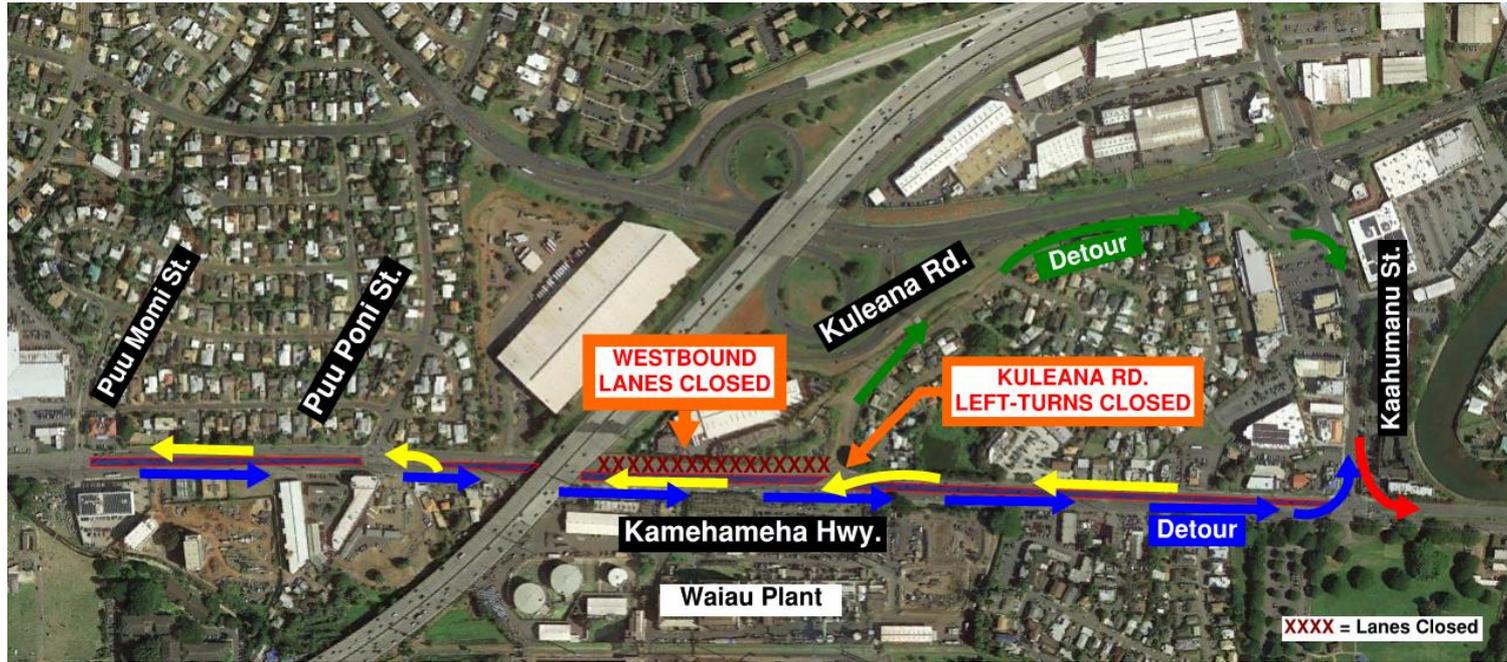

- Nightly westbound contraflow between Kuleana Road and Puu Poni Street for balanced cantilever structure through November 2016
- All left turns are closed at Kuleana Road
- Eastbound left turn detour is at Kaahumanu Street

Kamehameha Highway near Pearlridge

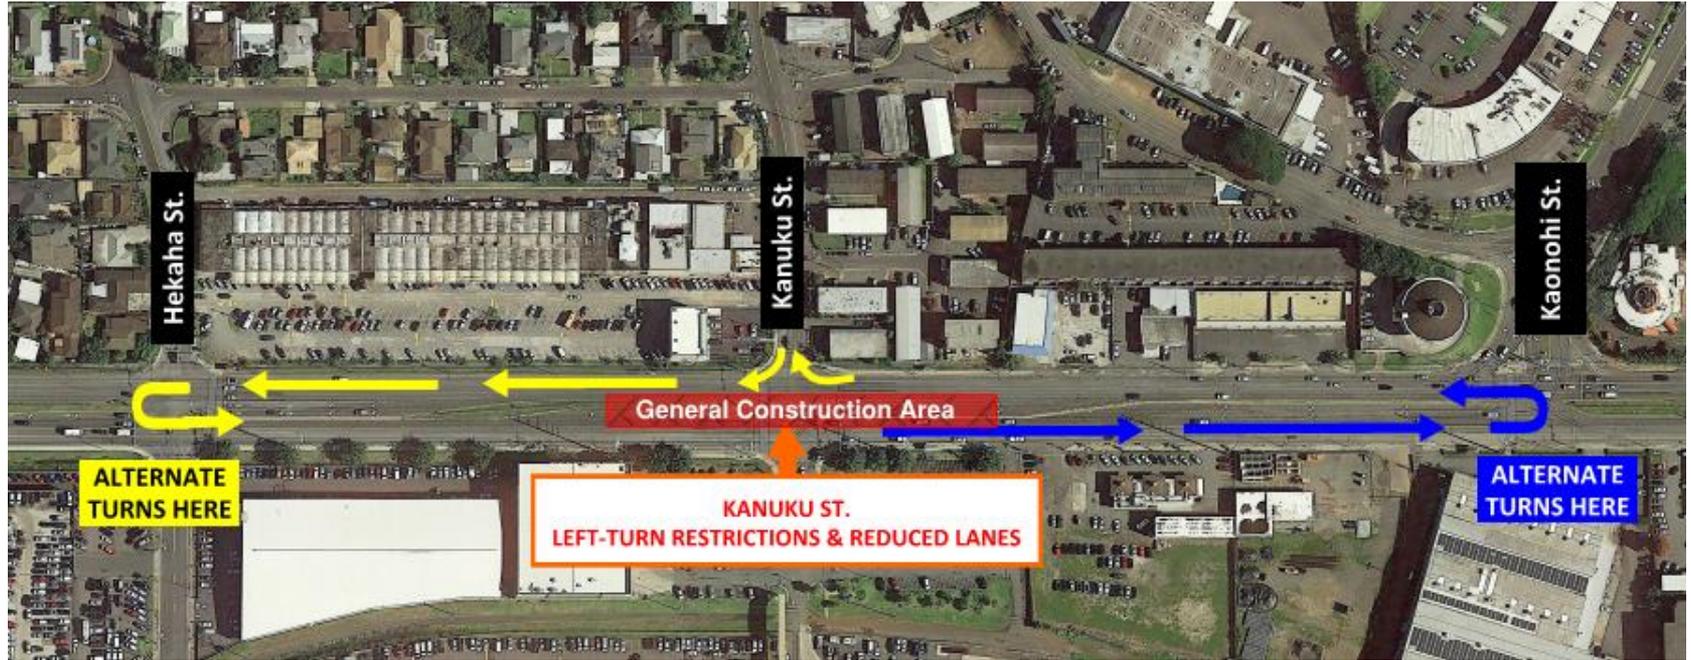

- Intersection closures during nighttime and daytime off-peak through first week of October 2016 at Kanuku Street for segment installation
- Left turn closures from late September through mid-October 2016
- Detours (U-turns) at Hekaha Street and Kaonohi Street

Kamehameha Highway in Aiea




- Full detours between Kanuku and Kaonohi Streets for utility and equipment removal work through November 2016
- Detour is along Moanalua Loop for eastbound and westbound directions

Kamehameha Highway in Aiea/Halawa



- 24/7 westbound contraflow near Moanalua Freeway for structures work through November 2016



Kamehameha Highway near Pearl Harbor

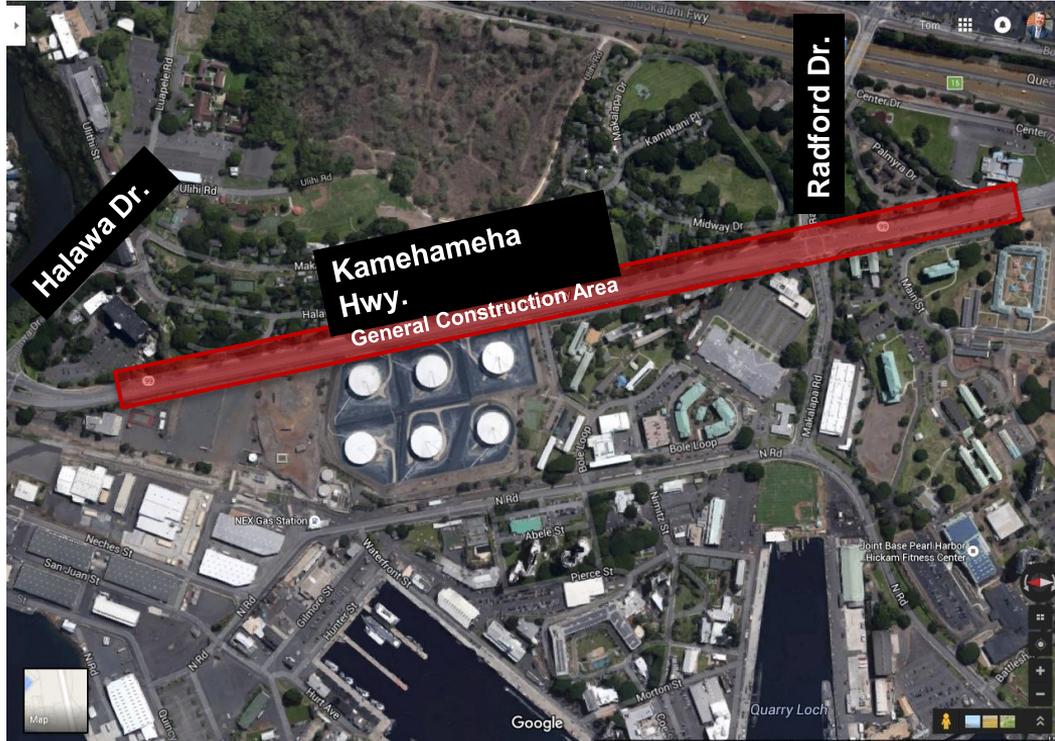

- Various daytime lane closures for utility relocation work through November 2016

Stay Connected

- Weekly Traffic Advisories
- Weekly e-Blast
- Website and Social Media
- Public Access Television Program



HART Rapid Response:

- 24-Hour Project Hotline number 808-566-2299
- Email Inquiries: info@HonoluluTransit.org
- Website Inquiries

Mahalo!
