



HART Board
Construction and Traffic Update
for October 27, 2016

West Oahu-Farrington Guideway, (Kapolei to Pearl Highlands), Kiewit Infrastructure West Co.

- KIWC is working to correct punch list items
- LCC Station work is on going
- KIWC is performing track on grade sub ballast and ballast for the track through LCC
- Projected Contract Completion: March 2017

West Oahu Stations Group (East Kapolei, UH West Oahu and Ho'opili), Nan Inc.

- 8% complete
- All drilled shafts at UHWO complete. Grading and compaction work ongoing for West Entrance Building.
- Falsework, formwork and concrete reinforcement ongoing at Ho'opili for platform girders and TCCR room. Conduit in TCCR room foundation also being installed.
- East Kapolei Station area being fenced in; drilled shaft work commencing late October.
- Contract Completion: March 2018

Farrington Highway Stations Group (West Loch, Waipahu Transit Center and LCC), Hawaiian Dredging Construction Co.

- All drilled shafts for West Loch station completed.
- Rebar installation at WLO ancillary building; building slab concrete poured.
- Began Vertical Raceway Conduit (VRC) at WLO
- Began installation of positive power line
- Contract Completion: January 2018

Maintenance and Storage Facility, Kiewit-Kobayashi Joint Venture

- Anticipated Final Acceptance Date has been changed to December 1, 2016, due to pending final documentation, anticipated isolation pad deliveries, ponding issues at the Operation and Service Building, and the anticipated arrival of the bogies to complete equipment testing.
- MSF Punch list Items – 99% (26 more items to be completed)

H2R2 Ramp, Royal Contracting Co.

- Excavation for retaining wall is complete. Installed rebar template at retaining wall footing
- Weeding activities were completed. Installation of stabilization matting can begin
- Contract Completion: October 2016

Pearl Highlands Transit Center and Parking Garage

- Solicitation in preparation

Kam Highway Guideway (Pearl Highlands to Stadium), Kiewit Infrastructure West Co.

- Construction of Balanced Cantilever Structure Sound walls (BCS) over H-1 are complete
- Heading #3 truss, at Pearlridge Station, to start demobilization this month.
- Contract Completion: May 2017

Kam Highway Stations Group (Pearl Highlands, Pearlridge and Aloha Stadium), Nan Inc.

- Notice To Proceed: October 3, 2016
- Work started at Pearl Highlands Station. Contractor will begin work at Pearlridge Station by the end of October 2016.
- Working on finalizing access at Aloha Stadium Station.
- Contract Completion: May 2019

Airport Utilities Construction, Nan Inc.

- Project Substantial Completion: October 7, 2016
- Punch list has been generated
- Closeout process is ongoing

Airport Guideway and Stations (Aloha Stadium to Middle Street)

- Awarded to Shimmick/Traylor/Granite Joint Venture on September 20, 2016
- Tentative Notice to Proceed (NTP) first week of November 2016

Core Systems, Ansaldo Honolulu Joint Venture


- 38% complete – Vehicles and Core Systems
- MSF activities 54% complete with anticipated completion of all TPSS and Signaling work by the end of the year.
- Train 2 is 88% complete and continues Water Testing and Initial Static Testing, Train 3 is 42% complete
- Contract Completion: March 2019
- Projected Completion: October 2025

Farrington Highway in Waipahu




- Various daytime and nighttime closures between Old Fort Weaver Road and Kahualii Street for finishing and traffic signal work through November 2016, except during Thanksgiving weekend.

Kamehameha Highway in Pearl City

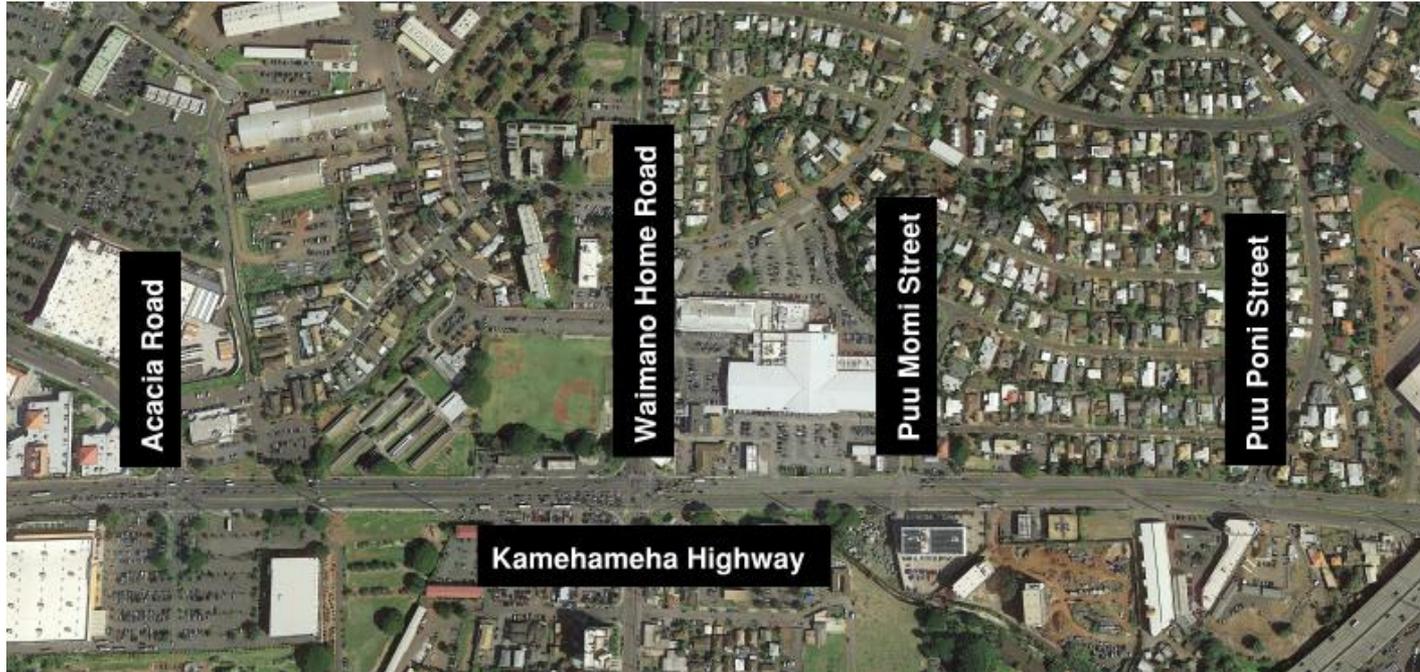


- Various daytime and nighttime closures between Acacia Road and Puu Poni Street for traffic signal work through November 2016, except during Thanksgiving weekend.

H-1 in Pearl City

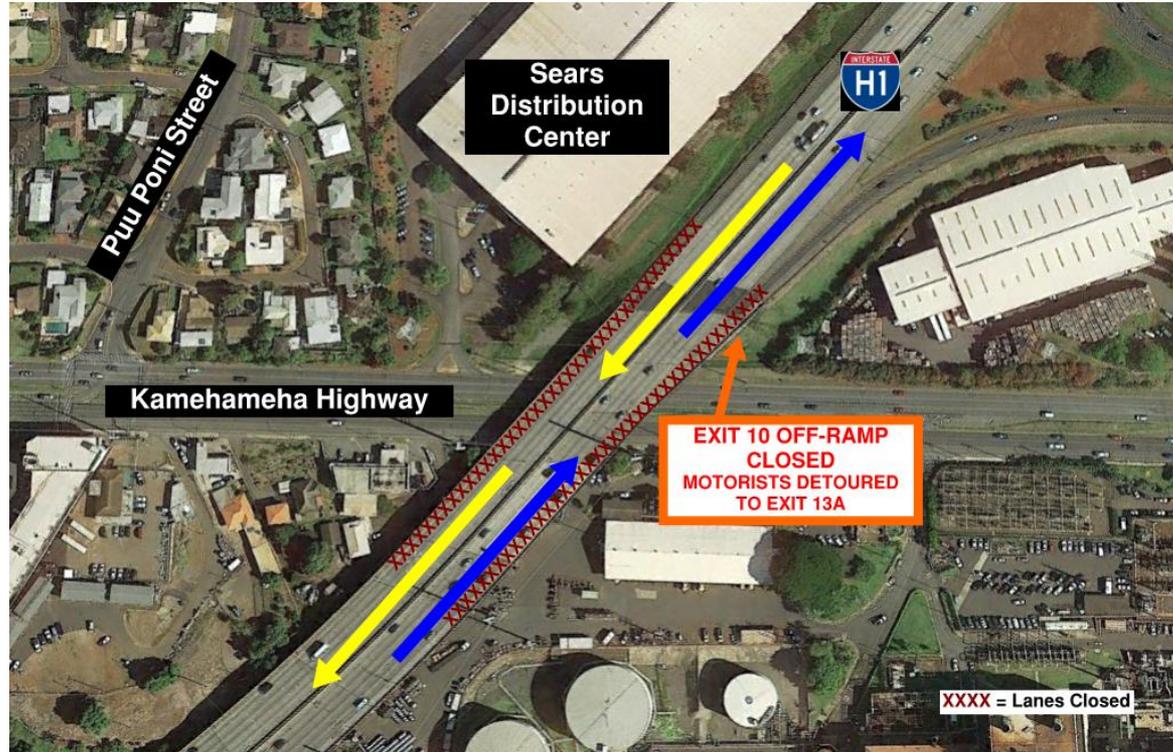

- Standard nightly closures on eastbound and westbound H-1 in Pearl City through November 2016, except during Thanksgiving weekend.

Kamehameha Highway in Pearl City

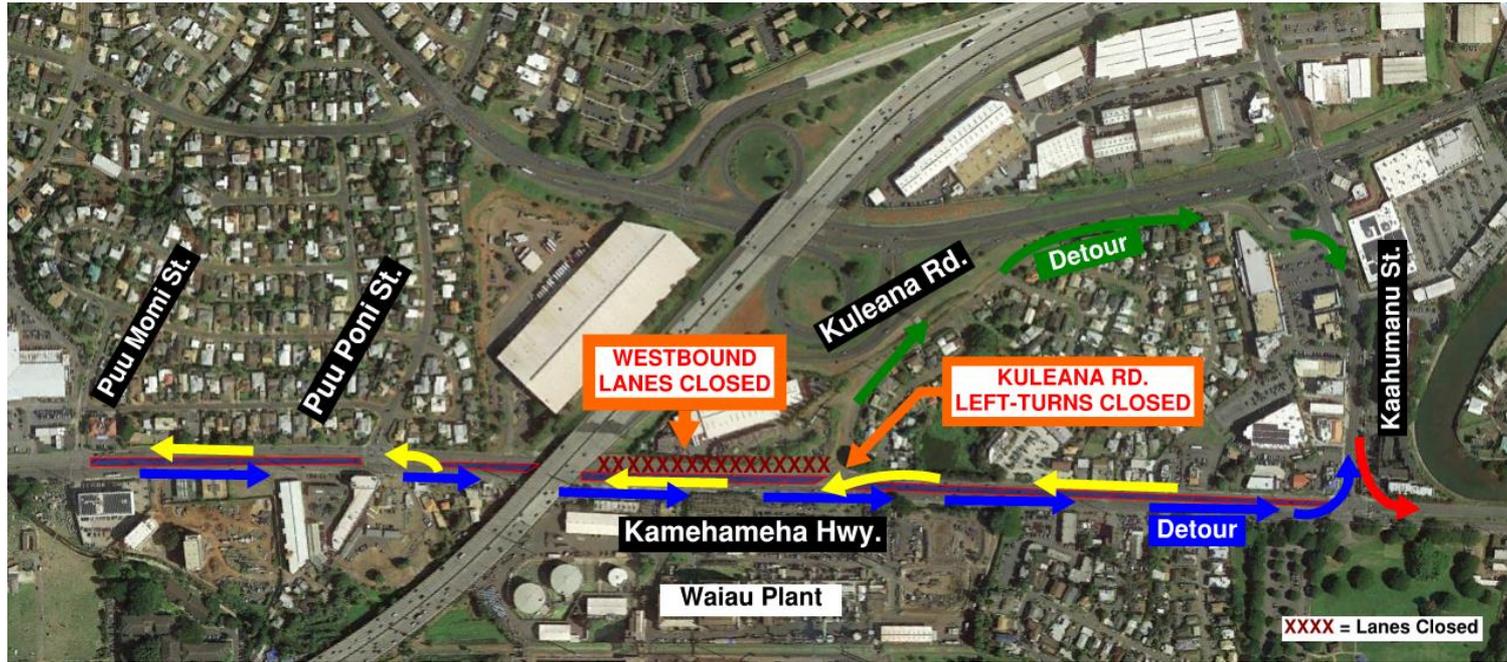

- Nightly westbound contraflow between Kuleana Road and Puu Poni Street for balanced cantilever structure through November 2016, except during Thanksgiving weekend.
- All left turns are closed at Kuleana Road
- Eastbound left turn detour is at Kaahumanu Street

Kamehameha Highway in Aiea



- Full detours between Kanuku and Kaonohi Streets for utility and equipment removal work through November 2016, except during Thanksgiving weekend.
- Detour is along Moanalua Loop for eastbound and westbound directions.



Kamehameha Highway in Aiea/Halawa



- 24/7 westbound contraflow near Moanalua Freeway for structures work through November 2016, except during Thanksgiving weekend.

Stay Connected

- Weekly Traffic Advisories
- Weekly e-Blast
- Website and Social Media
- Public Access Television Program



HART Rapid Response:

- 24-Hour Project Hotline number 808-566-2299
- Email Inquiries: info@HonoluluTransit.org
- Website Inquiries

Mahalo!
