

Right-of-Way Status Update May 12, 2016



Meeting our Goals

- Balance respect for property owner with schedule needs and project budget
- Balance responsibility of staying within the budget in a changing real estate market
- Continue to communicate and educate effectively
- Negotiate fairly
- Meet requirements of the Uniform Act




Status Summary

- ROW team continues to meet the schedule for City Center acquisitions relative to program procurement needs
 - > Intense focus on Airport and Dillingham Parcels to support upcoming procurement
- Current total site access available for contractor is 95% of the total area needed
- Eminent Domain pending
 - > 51 prior requests for authorization from HART Board
 - 2 parcels for resubmission to HART Board and City Council
 - > 1 parcel rejected by the City Council
 - > 6 cases filed
 - 1 settled prior to trial
 - 1 settled prior to trial, pending FTA approval
 - 2 parcels disputed
 - 2 condemnations to resolve title issues
 - > 35 properties in escrow



Progress Site Access Available by Land Area

as of 4/11/2016

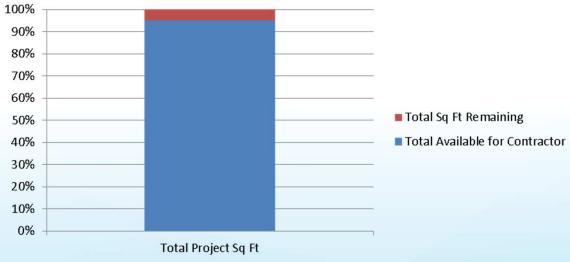


otal Projec Sq Ft	Total Sq Ft Requirement	14,665,681		
	Total Available for Contractor	13,936,629		
	Total Sq Ft Remaining	729,052		
	% Available for Contractor	95%		
	Reported Last Month	95%		



Progress Site Access Available to Contractors by Land Area by Section


as of 4/11/2016

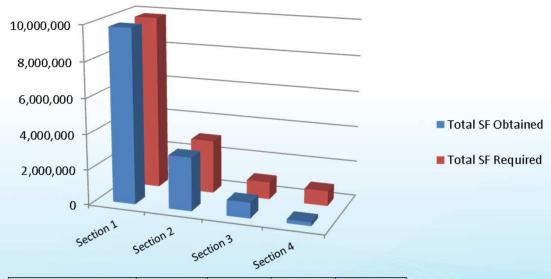

	Section 1	Section 2	Section 3	Section 4
Total SF Obtained	9,808,840	3,023,851	891,152	212,786
Total SF Required	9,808,840	3,027,319	979,875	849,647
% Progress	100.00%	99.89%	90.95%	25.04%




Parcel Site Control Status by Land Area and Parcels as of 4/11/2016

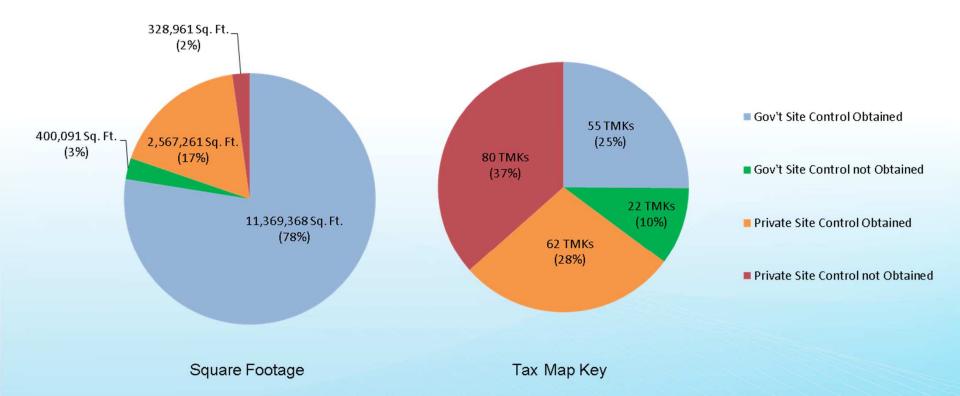



Acquisition Status by Land Area and Parcels

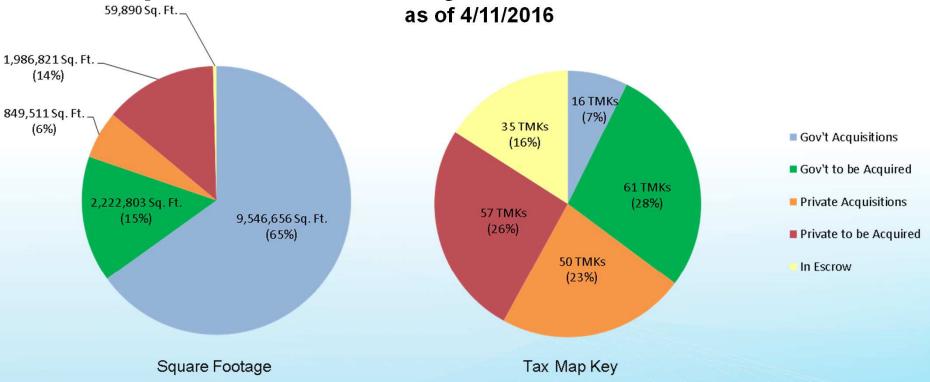



Recent Accomplishments

- Acquisition for owner of 13 parcels 12 in escrow and 1 escrow closed
- 3 Land Court Subdivisions Maps approved
- Civic Center Station site acquired
- Navy Pearl Harbor Station site acquired
- 2 HECO utility relocation right-of-entry executed
- 2 Possession and Use Agreement executed



Right-of-Way Cost Estimate Update

as of 4/11/2016

	Budget	Expended	Remaining Budget Balance	Estimate to Completion	Forecast Variance		
Acquisition	\$201.70	\$90.60	\$111.10	\$98.00	\$13.10		
Relocation	\$20.50	\$11.00	\$9.50	\$15.50	(\$6.00)		
Total (Million)	\$222.20	\$101.60	\$120.60	\$113.50	\$7.10		

Notes:

- Administrative overhead costs aggregated with the Acquisition and Relocation numbers
- Estimate to completion based on offers, appraisals or assessed values



Right-of-Way Risks to Budget

- Volatility of Real Estate Market, especially in the Kakaako - Ala Moana area
- Conversions from partial acquisition to full acquisition
- Unanticipated relocation costs for complex relocations, particularly unexpected full takes



Private Property Acquisition Summary as of 4/11/2016


ю	тмк	Take	Address	Owner	Recordation Date	Settlement (\$)	Total Acquisition (\$)	FFGA Budget	Note	Remaining Balance in Budget
1	1-1-016-005	Full	2676 Waiwai Loop	2676 Waiwai Loop LLC	7-Mar-14	4,900,000	4,924,144	6,173,973		1,249,829
2	1-1-016-006	Full	2668 Waiwai Loop	Alert Holding Group	28-Mar-14	3,900,000	3,918,089	4,648,445		730,356
3	1-1-016-014	Full	479 Lagoon Drive	Chevron USA Inc	21-Mar-14	2,825,000	3,042,274	3,930,328		888,055
4	1-1-016-015	Full	515 Lagoon Drive	Brewer Trust	3-Jun-13	3,540,000	3,551,508	5,067,659		1,516,15
5	1-1-016-016	Full	2613 Waiwai Loop	International Express Inc	5-Jan-16	5,936,000	6,062,548	472,448	2	-5,590,10
6	1-2-003-016	Full	1819 Dillingham Boulevard	Strain	21-Apr-14	1,100,000	1,106,416	1,741,689		635,27
7	1-2-003-017	Partial	1815 Dillingham Boulevard	Hernandez	11-May-15	150,308	151,758	111,258		-40,50
8	1-2-003-018	Partial	1803 Dillingham Boulevard	Rosebud Holdings Ltd	14-Aug-15	140,589	142,407	261,258		118,85
9	1-2-003-020	Partial	1727 Dillingham Boulevard	Elum Two LLC	7-Dec-15	216,245	220,540	364,465		143,92
10	1-2-003-082	Full	1825 Dillingham Boulevard	Nguyen	31-Jul-14	980,000	984,299	1,596,625		612,32
11	1-2-003-101	Partial	1701 Dillingham Boulevard	Fujii Trustee	16-Nov-15	455,000	458,234	463,178		4,94
12	1-2-009-001	Full	1901 Dillingham Boulevard	Sebastian LLC	16-Aug-12	2.800.000	2.805.135	2.814.000		8.86
13	1-2-009-100	Full	1953 Dillingham Boulevard	Sebastian LLC	16-Dec-14	2,250,000	2,257,359	436,620	2	-1.820.73
14	1-2-009-101		Subdivided TMK 1-2-009-017 into 10			_,,		,		.,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,,
15	1-2-009-018	Full	1927 Dillingham Boulevard	Rodrigues/Hinch	18-Nov-14	800,000	804.686	261,258	2	-543,42
16	1-2-010-068	Full	1900 Dillingham Boulevard	Kam Trust	4-Dec-12	1,825,000	1,831,279	2,529,000	Ė	697,72
17	1-5-007-021	Full	545 Kaaahi Street	Nuuanu Auto	11-Oct-14	2,275,000	2,285,004	2,819,500		534.49
18	1-5-007-023	Full	533 Kaaahi Street	KWA/ Abrams	23-Apr-10	2,850,000	2,850,000	2,850,000	1	- 00 1, 10
19	1-5-028-073	Partial	1617 Dillingham Boulevard	Fujii Trustee	13-Oct-15	255,000	258,439	179,373	L'	-79,06
20	1-7-002-026	Full	902 Kekaulike Street	902 Partners Ltd	1-Nov-12	5,200,000	5,219,351	4,927,000	2	-292.3
21	2-1-030-050	Easement	573 Halekuwila Street	Henry Domen Trust	25-Feb-16	45,000	46,930	4,927,000	4	-46.9
22	2-1-030-053	Partial	555 South Street	Bishop Estates	7-Apr-16	3.705.000	3,715,787	3.166.007	-	-549.78
23	2-1-030-053	Easement	598 Halekauwila Street		18-Dec-15		102,406	179,517	3	
24	2-3-004-048	Full	1156 Waimanu Street	Aoyagi Trust Young	21-Mar-12	1,720,000	1,730,578	1,730,578	3	77,1
										0.00
25	2-3-004-069	Full	1168 Waimanu Street	Cody Prop LLC	10-Feb-12	2,650,000	2,660,398	2,658,317	\vdash	-2,0
26	2-3-007-033	Full	1169 Kona Street	Kakaako Associates	13-Oct-14	5,800,000	5,825,106	10,102,669		4,277,56
27	2-3-007-036	Full	1174 Waimanu Street	McArthur Trust/Hideko	8-Oct-14	1,400,000	1,407,845	1,951,386	\vdash	543,5
28	2-3-007-039	Full	1163 Kona Street	Nelson Family Trust	1-Dec-15	3,000,000	3,010,960	2,644,402	\vdash	-366,5
29	2-3-007-044	Full	1201 Kona Street	ROKH Holdings Inc	3-Oct-14	1,350,000	1,357,540	1,751,700	\vdash	394,1
30	2-3-007-054	Full	1246 Kona Street	Taran Trust	15-May-15	1,100,000	1,105,634	1,439,263		333,6
31	9-4-017-011	Full	94-818 Moloalo Street	Okazaki	4-Aug-11	870,000	870,000	870,000	1	
32	9-4-019-050	Full	94-819 Farrington Highway	Min	1-Aug-12	1,000,000	1,004,277	1,005,000		7:
33	9-4-047-008	Partial	94-144 Farrington Highway	Robinson LLC	13-Mar-15	887,816	898,742	743,278		-155,4
34	9-4-048-046	Full	94-119 Farrington Highway	Cutter Dev.	25-Jul-11	3,155,000	3,159,142	3,159,142	1	
35	9-4-048-047	Full	94-136 Leonui Street	Cutter Dev.	25-Jul-11	2,745,000	2,749,142	2,749,142	1	
36	9-6-003-012	Full	96-171 Kamehameha Highway	Alpha Omega	29-Jun-11	287,000	287,030	287,030	1	
37	9-6-003-013	Full	96-165/169 Kamehameha Highway		7-Sep-11	454,000	455,588	455,588	1	
8	9-6-003-014	Full	96-157 Kamehameha Highway	Bala	27-Jun-11	1,214,000	1,216,787	1,216,787	1	
39	9-6-003-015	Full	96-159 Kamehameha Highway	Bala	10-Aug-11	53,000	53,304	53,304	1	
10	9-6-003-016	Full	96-149A Kamehameha Highway	Bala	10-Aug-11	22,000	22,304	22,304	1	
11	9-6-003-017	Full	96-149 Kamehameha Highway	Farinas	15-Sep-11	558,000	559,914	559,914	1	
12	9-6-003-018	Full	96-137 Kamehameha Highway	Alipio/Solmirin	25-Jan-12	1,015,000	1,017,915	1,017,915	1	
13	9-6-004-002	Full	96-93 Kamehameha Highway	Kawano	5-May-11	790,000	790,000	790,000	1	
14	9-6-004-017	Full	Kamehameha Highway	Suenaga	29-Jun-11	90,000	90,000	90,000	1	
15	9-6-004-023	Partial	Waihona Street	Bishop Estates	4-Aug-15	22,300	24,476	157,965		133,4
16	9-7-023-008	Partial	945 Kamehameha Highway	Stuart Plaza Inv	26-May-15	300,000	300,000	151,344		-148,6
17	9-7-024-034	Easement	1000 Kamehameha Highway	ABP Pearl Highlands LLC	19-Jan-16	41,199	42.837	679,106	3	636,2
18	9-8-009-017	Full	98-077 Kamehameha Highway	Continental Inv. Ltd	14-Jun-13	2,500,000	2,509,030	3,512,500	Ť	1,003,4
		Full	98-080 Kamehameha Highway	50th State Prop.	1-May-12	6.010.000	6,027,021	6.027.021	1	.,250,1
LQ.										
19	9-8-010-002 9-9-003-068	Full	99-140 Kohomua Street	RCJ	13-Sep-11	991.000	993,783	993,783	1	

Notes:

- Baseline assumes zero variance (budget = actual) during FFGA approval process.
- ** Cost exceeded budgeted amount due to conversion from partial to full acquisition. Bold print reflects most recent acquisition



Private Property Acquisition Cost as of 4/11/2016

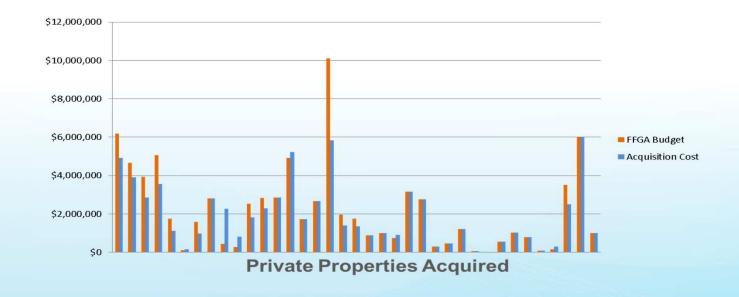



Mahalo!



