ID	Task Name	Start	Finish	Predecessors	Duration	Free Slack
1	***PA SIGNED DECEMBER 13***	***Fri 11/13/09***	***Fri 11/13/09***		***0 days***	***78 days***
2	**Airport Coordination**	**Mon 8/17/09**	**Fri 11/6/09**		**82 days**	**84 days**
3	Coordination Meeting	Mon 8/17/09	Mon 8/17/09		0 days	0 days
4	Address Runway Clearance	Mon 8/17/09	Fri 10/23/09		68 days	98 days
5	Address Terminal Area Alignment	Wed 9/23/09	Wed 10/7/09		15 days	114 days
6	FAA Agreement	Fri 11/6/09	Fri 11/6/09		0 days	26 days
7	**Section 4(f) Resources**	**Tue 8/18/09**	**Fri 11/13/09**		**88 days**	**77 days**
8	Submit Draft Letter to State to send NPS for Aloha Stad	Tue 8/18/09	Tue 8/18/09		0 days	165 days
9	State Submit Letter to NPS for Aloha Stadium Review	Fri 9/25/09	Wed 10/7/09		13 days	114 days
10	NPS Review	Sat 10/10/09	Fri 10/23/09		14 days	98 days
11	Aloha Stadium Approval by NPS	Fri 11/13/09	Fri 11/13/09		0 days	19 days
12	**Section 106**	**Tue 7/28/09**	**Fri 12/4/09**		**129 days**	**57 days**
13	Complete Section 106 Programmatic Agreement	Tue 7/28/09	Fri 11/13/09		109 days	20 days
14	Council Committee Recommendation to CC	Mon 10/26/09	Mon 10/26/09		1 day	95 days
15	City Council Approval of DTS Signature Authority	Tue 10/27/09	Tue 10/27/09		1 day	37 days
16	Final PA signed by City, FTA, DLNR, ACHP, and Signat	Fri 12/4/09	Fri 12/4/09	13,15	0 days	0 days
17	**FTA FEIS Review and Approval**	**Thu 10/15/09**	**Thu 12/3/09**		**50 days**	**0 days**
18	FTA Review of Final EIS	Thu 10/15/09	Wed 11/11/09		28 days	9 days
19	Legal Sufficiency Review by FTA	Thu 10/15/09	Fri 11/20/09		37 days	0 days
20	Incorporate Legal and EIS Review by FTA	Sat 11/21/09	Wed 11/25/09	19,18	5 days	7 days
21	FTA approval of Final EIS	Thu 12/3/09	Thu 12/3/09	20,11,6	1 day	0 days
22	**Produce and Distribute Final EIS**	**Fri 12/4/09**	**Fri 12/18/09**		**15 days**	**0 days**
23	Final Production	Fri 12/4/09	Mon 12/7/09	21,16	4 days	0 days
24	Print and distribute FEIS	Tue 12/8/09	Thu 12/10/09	23	3 days	0 days
25	Submit FEIS to QEQC	Thu 12/10/09	Thu 12/10/09	24	0 days	0 days
26	Submit NOA to EPA	Fri 12/11/09	Fri 12/11/09	24	1 day	0 days
27	NOA - Publish Date in Federal Register	Fri 12/18/09	Fri 12/18/09	26FS+7 days	0 days	0 days
28	OEQC Review and Governor Signs	Fri 12/11/09	Sat 1/9/10	25	30 days	19 days
29	FTA Reconciliation of Comments	Mon 1/18/10	Thu 1/28/10	27FS+30 days	11 days	0 days
30	ROD - Publish Date in Federal Register	Fri 1/29/10	Fri 1/29/10	29,28	1 day	0 days

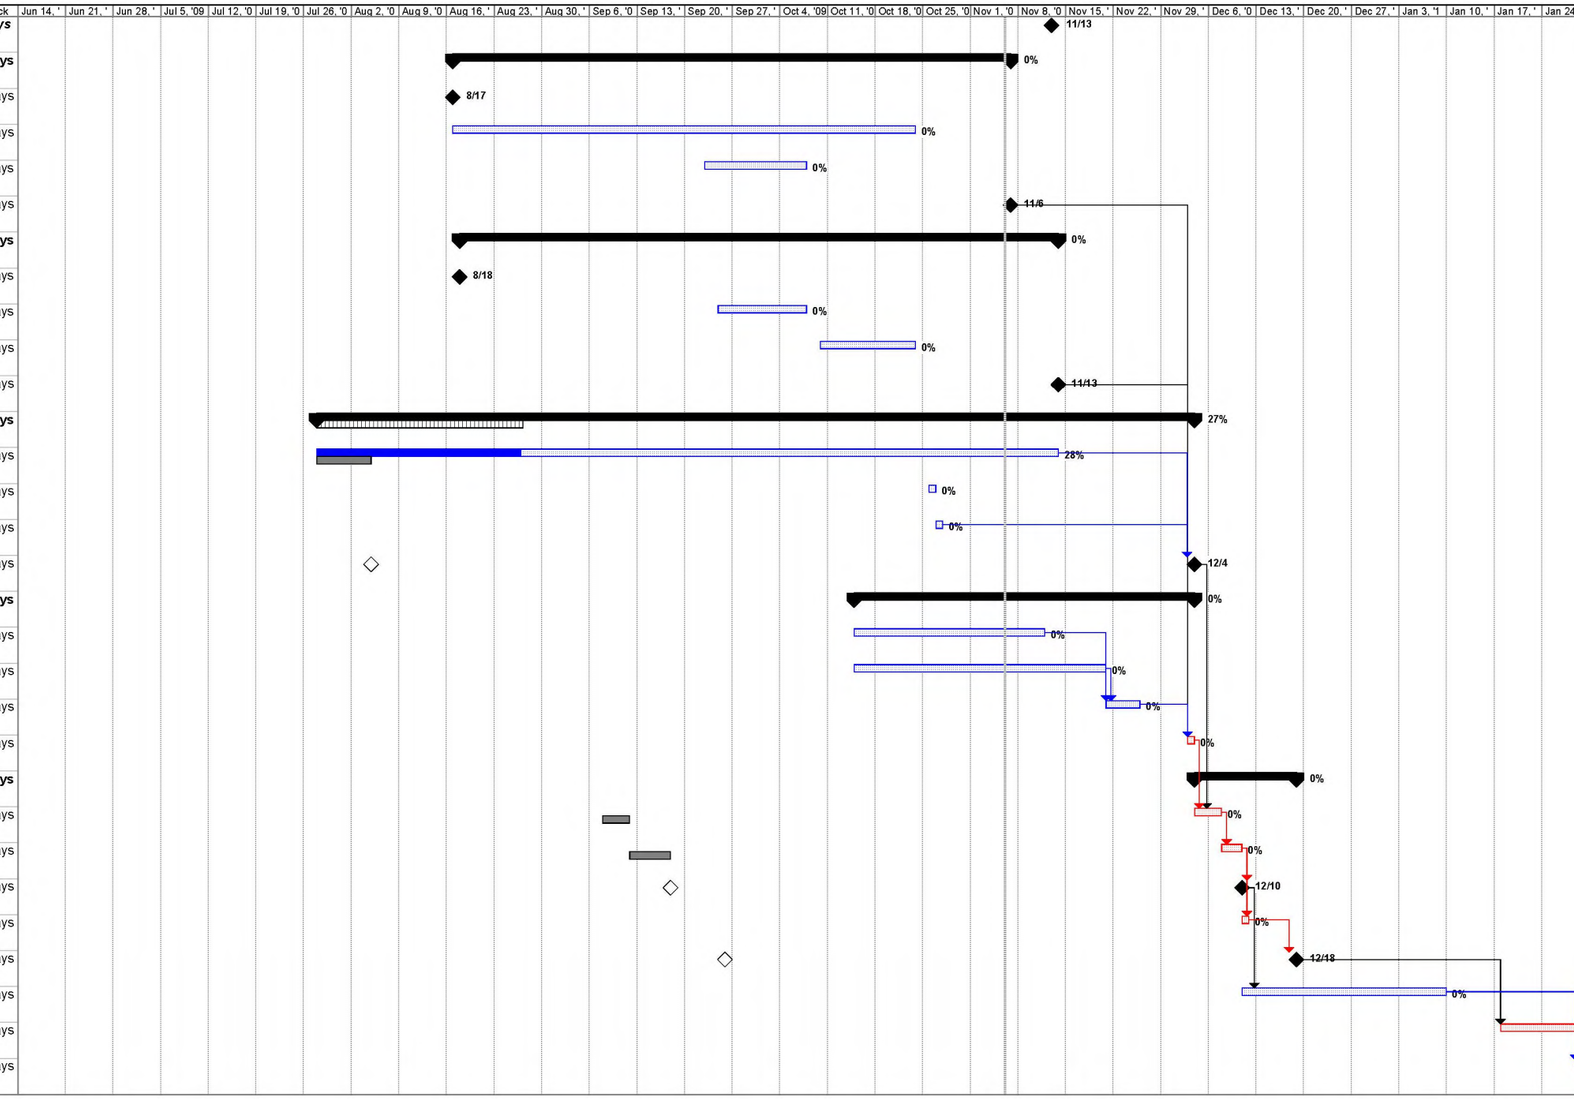

Project: PA SIGNED DECEMBER 4
Date: Fri 11/6/09

Critical | Critical Progress | Split | Baseline | Baseline Milestone | Summary Progress | Project Summary | External Milestone
Critical Split | Task | Task Progress | Baseline Split | Milestone | Summary | External Tasks | Deadline
